

# Ickleford Mill Demolition Stage Construction Management Plan

Subject: Construction Management Plan

---

Section 1: Introduction to the project – include resident liaison details

Section 2: Site Layout, significant points

Section 3: Main duty holders

Section 4: Contractor's selection procedure

Section 5: Activities with risks to Health and Safety and the Environment

Appendices

## Section 1: Introduction to the project

Ickleford Mill

Enabling works and demolition of existing buildings on the former Ickleford Mill project.

### PROJECT INFORMATION

#### SITE ADDRESS

##### Hill Site

*Ickleford Mill  
Arlesey Road  
Hitchin  
Herts  
SG5 3UN*

*What3words reference: ///squashes.tadpole.foresight*

*T: 0208 527 1400*

**Details of Nominated Resident Liaison Representative to be circulated to those residents consulted on the application. This person will act as first point of contact for residents who have any problems or questions related to the ongoing development.**

*Resident Liaison Manager – Kelly Player  
24/7 Resident contact number: 08000326760  
Email: [residents@hill.co.uk](mailto:residents@hill.co.uk)  
Address: The Powerhouse  
Gunpowder Mill  
Powdermill Lane  
Waltham Abbey  
Essex  
EN9 1BN*


SITE LOCATION PLAN

*Site Close Up:*



Subject: Construction Management Plan

*Local Area Detail:*

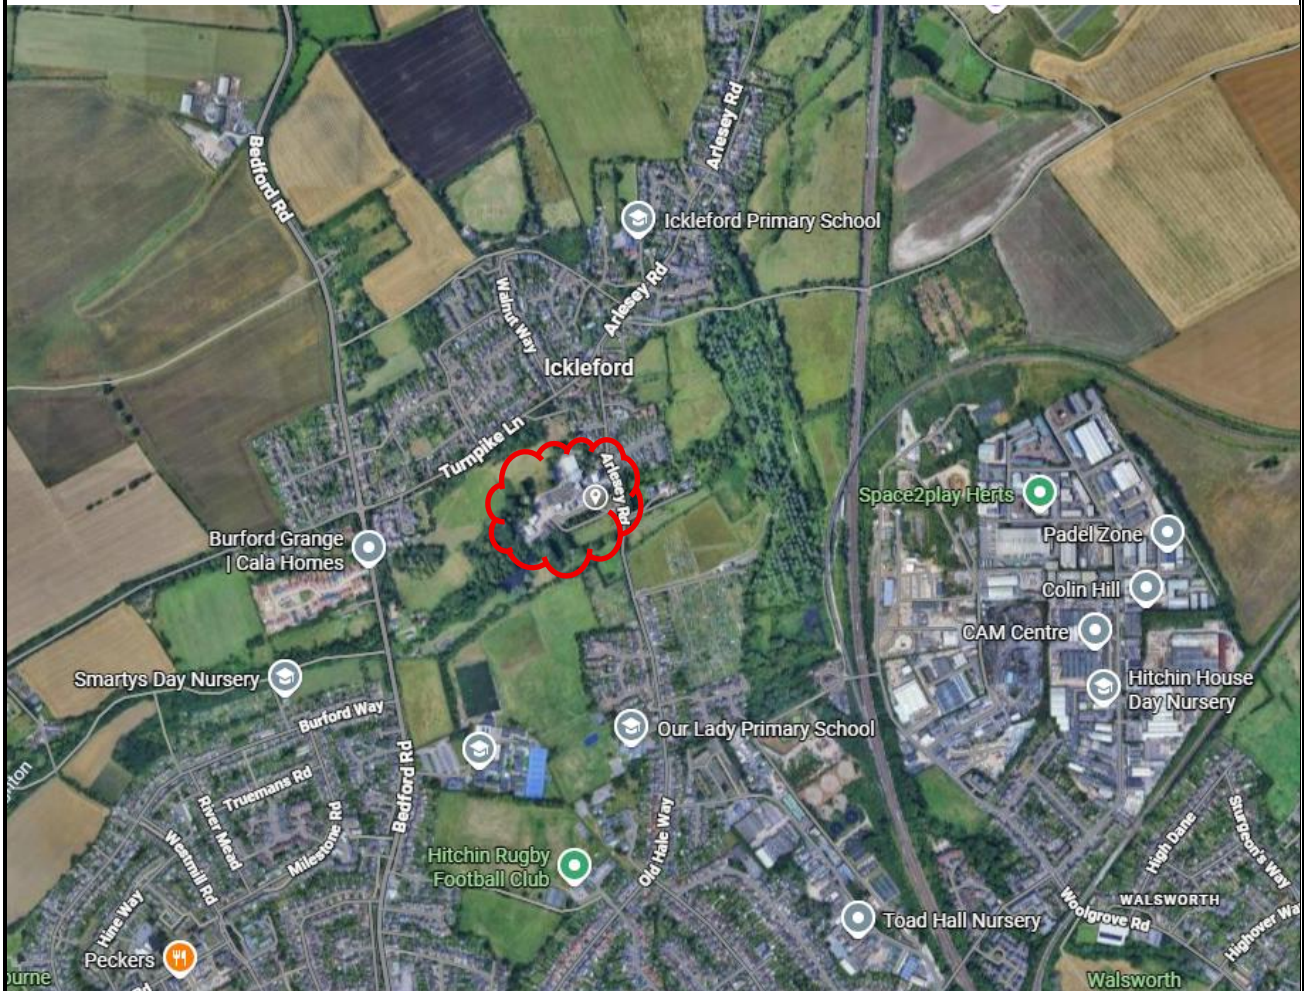

#### BRIEF DESCRIPTION OF THE SITE:

The Ickleford Mill site is situated on the Southern border of the village of Ickleford, located to the North of Hitchin, Hertfordshire. The site was utilised as a mill for many years prior to closing in 2016. The site comprises of various structures such as silos, office buildings and warehousing and hardstanding.

The site is bordered by green fields to the Southern and Western boundaries and most of the Northern boundary. Part of the Northern boundary and across Arlesey Road to the Eastern boundary lay residential properties.

A watercourse, the River Oughton runs through the development.

#### DESCRIPTION OF THE PROPOSED WORKS:

Enabling works, including Site fencing, temporary offices and tree cutting / removal. Demolition of existing structures, removal of hardstanding and crushing of materials. Removing from site any materials that cannot be later recycled on site.

## Section 2: Site Layout, significant points

| SITE LAYOUT - SIGNIFICANT POINTS                                                                                                                                                                                                                                                                             |  |
|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--|
| Access/Egress:                                                                                                                                                                                                                                                                                               |  |
| <p>Access / Egress shall be through the existing site access off Arlesey Road. Both existing site gates, situated off the same access point, shall be utilised for deliveries and muck away.</p>                                                                                                             |  |
| Compound:                                                                                                                                                                                                                                                                                                    |  |
| <p>For initial site set up: A first compound and welfare set up shall be placed by the entrance, and an Oasis unit will be in place.</p> <p>Initial parking throughout the enabling and demolition phases shall utilise existing hardstanding within the development as shown on the attached site plan.</p> |  |

|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                               |  |
|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--|
| Materials Storage:                                                                                                                                                                                                                                                                                                                                                                                                                                                                            |  |
| <p>Materials shall be delivered into site in accordance with the traffic management plan and unloaded in the designated areas. Whilst minimal materials will not be required during the enabling and demolition phases, they shall be set down utilising existing site hardstanding areas.</p> <p>Plant shall be delivered to site within working hours and loaded / unloaded in a safe manner.</p>                                                                                           |  |
| Build Sequence:                                                                                                                                                                                                                                                                                                                                                                                                                                                                               |  |
| <p>Works shall commence with the erection of site hoarding and herras fencing to boundaries and within site to protect the watercourse. Tree works shall be carried out to cut back / remove any trees / vegetation as required. Demolition shall be carried out to remove all superstructures on the development before foundations and hardstanding are removed. All onsite hardcore shall be crushed on site and left in heaps, to be utilised during further development of the site.</p> |  |
| Security Hoardings:                                                                                                                                                                                                                                                                                                                                                                                                                                                                           |  |
| <p>A mixture of ply hoarding, to most prominent areas, herras on timber posts and herras on feet shall be used to secure the site. All main entrances shall have metal gates, kept locked when not in use. Hoardings shall be painted in company colours and decorated with sales branding where appropriate. All fencing shall be regularly inspected to insure it is kept to a safe, well-maintained standard.</p>                                                                          |  |
| Construction Vehicles:                                                                                                                                                                                                                                                                                                                                                                                                                                                                        |  |
| <p>Material deliveries will be ridged and /or articulated lorries. Plant shall be delivered on low – loaders. Muck away shall be carried out with 8-wheel 20 Tonne lorries. Construction workers will arrive in either cars or vans. Car sharing shall be encouraged to reduce the number of vehicles on site as much as possible.</p> <p>Estimated 1 – 10 deliveries per day. 5 – 20 construction cars / vans.</p>                                                                           |  |
| Public Rights of Way:                                                                                                                                                                                                                                                                                                                                                                                                                                                                         |  |
| <p>No public rights of way on site.</p>                                                                                                                                                                                                                                                                                                                                                                                                                                                       |  |

## Section 3: Main duty holders

### Client

Name Hill Residential  
Address The Courtyard  
Abbey Barns  
Ickleton  
Postcode CB10 1SX  
Phone 01223 792700

### Principal Contractor

Name Hill Partnerships Ltd  
Address The Power House,  
Gunpowder Mill,  
Powdermill Lane,  
Waltham Abbey,  
Essex  
Postcode EN9 1BN  
Phone 020 8527 1400  
Fax 020 8501 8770

### CDM Designer

Name Hill Partnerships Ltd  
Address The Power House,  
Gunpowder Mill,  
Powdermill Lane,  
Waltham Abbey,  
Essex  
Postcode EN9 1BN  
Phone 020 8527 1400

### Architect

Name Hill Residential  
Address The Courtyard  
Abbey Barns  
Ickleton  
Postcode CB10 1SX  
Phone 01223 792700

### Engineers

Name Superstructures  
Address Cranes Farm Road, Basildon  
Postcode SS14 3JJ  
Phone 01268 530500

## Section 4: Contractor's selection procedure

### CONSTRUCTION (DESIGN AND MANAGEMENT) REGULATIONS 2018

#### PROCEDURE FOR PRE-ASSESSING CONTRACTORS/SUB-CONTRACTORS

The CDM Regulations require that the Principal Contractor makes 'reasonable enquiries' to establish the commitment to health and safety and the ability and resources to manage health and safety of contractors. It is also necessary for the Principal Contractor to be able to demonstrate that the 'reasonable enquiries' have been made to ensure compliance with Appendix 4 core criteria for pre assessing sub contractors. As a minimum the following will be carried out to meet these statutory duties:

#### 1 INTRODUCTION

- 1.1 The Hill ("The Company") recognises that there is a legal requirement to ensure that they only appoint subcontractors who have the necessary health and safety competence and resources to carry out their work in a safe manner.
- 1.2 We are committed to engaging our subcontractors in jointly promoting the continuous improvement of our health and safety performance, and we are determined that everyone employed on our projects will be suitably informed, supervised and competent to carry out their duties.
- 1.3 The Company has Preferred Lists of Subcontractors who are selected and appointed in line with company procedures and who have demonstrated technical and health and safety competence.
- 1.4 The detailed subcontract procedures and guidance on their implementation are available on Intranet – Safety.

#### 2 SCOPE

- 2.1 The subcontract procedures are applicable to contractors and designers who would be engaged in the undernoted processes.
  - Concept and feasibility studies.
  - Planning.
  - Outline Design.
  - Detailed Design.
  - Construction and Installation.
  - Commissioning.
  - Maintenance.

3 Pre-qualification Assessment

- 3.1 Management must ensure that any prospective subcontractor, not already approved by the Company, has the necessary health and safety arrangements in place to support us to the required level.
- 3.2 The Company Performa "Subcontractors Health and Safety Assessment for Acceptance for Approved Subcontractor" must be completed for each subcontractor (Appendix HS/05/02). If the subcontractor is deemed to have suitable health and safety competencies they should be graded in terms of their arrangements and the scope of their activities.
- 3.3 There are three grading levels, with Grade 1 being a subcontractor who is competent to manage the health and safety aspects of their activities; Grade 2 being a subcontractor who has health and safety arrangements in place, but who requires input from Hill; and Grade 3 who are subcontractors who are not approved to work within the Hill.
- 3.4 The pre-qualification and selection process will normally be conducted and managed by a person appointed by the Divisional Director at Regional Offices, it is therefore vital that the relevant information is passed onto Project Managers.

The Performa representing the summary of a detailed operation process. A fully documented file in support of the assessment must be maintained in divisional records.

- 3.5 The pre-qualification process relates to the first application to be included on the Preferred List, thereafter re-submissions will be at the Company's discretion.

### INFORMATION FOR CONTRACTORS

So far as it is relevant to the activities of particular contractors and so far as information is available, sections of the Health and Safety Plan, together with design information and the health and safety standards that apply, are presented as a part of the tendering documentation. Subsequent to appointment and as it becomes available relevant information is passed to the contractor to facilitate the compilation of pertinent risk assessments/method statements.

## SELECTION PROCEDURES

### 1. CONTRACTORS AND DESIGNERS

Hill select contractors, designers and sub-contractors from those who, from previous experience, are known to adopt an approach to health and safety that is commensurate with the stringent criteria imposed by the company. Those where there is no previous experience are subjected to an enquiry procedure prior to being considered for selection. The criteria adopted in these cases are summarised as follows:

#### a) DESIGNERS SUB-CONTRACTORS

A primary requirement is membership of a bona fide professional body. This must be supported by successful experience in the type of contract and environment for which the designer is being considered. Sufficient suitable qualified people and sufficient resources must be available to enable the standards imposed to be achieved and the designer must have adequate knowledge of health and safety and associated legislation.

#### b) CONTRACTORS/SUB-CONTRACTORS

When considered against the degree of inherent risk, which the contract contains, a contractor/sub-contractor, to be eligible, must be able to demonstrate:

- A commitment to the health and safety philosophy
- A capacity to manage health and safety adequately by on site supervision
- The ability and resources necessary to develop and implement the health and safety plan and to deal with high risk elements
- The ability and resources necessary to ensure compliance with the health and safety regime of the project

### 2. MATERIALS AND SUBSTANCES

Within the contracts undertaken by Hill reasonable efforts are made to use only materials and substances that are low risk so far as the user, others who may be affected and the end user are concerned. In all cases the duties imposed by the COSHH Regulations are fulfilled. During the construction phase all necessary COSHH assessments are provided by the relevant sub-contractor and copies maintained on site. Information concerning hazardous materials and substances, which cannot be avoided by substitution, is incorporated into the Health and Safety File.

### 3. MACHINERY AND PLANT

The site management must check all machinery and plant supplied for use on the project, before it can be used. Particular inspection items include:

- Suitability of the item when considered against the use for which it is intended
- The availability and validity of documentation provided with the item The general serviceability of the item and where it is necessary, the availability of a suitably trained and qualified operator

- Stored fuels are to have designated areas and suitable bunds for drip trays and spills which are to be maintained and cleared when necessary, which may also require diesel spill kits under the Group Environmental Policy

During use plant and machinery is regularly monitored to ensure continued serviceability and the operator is observed to ensure competence and to avoid malpractice.

All machinery and plant must comply with the Provision and use of Workplace Equipment Regulations 1998 and/or any subsequent amendments.

## Section 5: Activities with risks to Health and Safety and the Environment

### SITE WIDE ACTIVITIES

Activities with site wide implications, e.g. traffic control, materials storage and movement, access routes, site security and personal safety, etc., and activities which may affect the general public, are planned prior to the project commencing. Management of these is a component of the management of the site and is monitored during safety visits by the Safety Advisor/Manager.

Operational activities are assessed in writing by the project management team to determine hazards and risks. Contractors are required to carry out detailed risk assessments and to produce methods by which identified risks may be either avoided or minimised. Certain high-risk operations, e.g. demolition, deep excavation, working in confined spaces, etc., are exempt from this procedure since they will automatically require detailed method statements to be produced.

Before the operations are allowed to commence, the methods proposed are submitted to the site management for agreement and, in the case of all high-risk activities, must be formally approved by the Safety Manager.

These can include:

- Storage and distribution of materials
- Movement of vehicles on site, particularly as this may affect pedestrian and vehicular safety
- Control and disposal of waste
- Provision and use of common means of access and places of work for all on site staff and visitors
- Provision and use of mechanical plant, which is used by a number of contractors
- Provision and use of temporary support services
- Temporary support structures, e.g. falsework
- Commissioning, including use of permits, etc.
- Protection from falling materials
- Exclusion of unauthorised people
- Protection of the public/information for local residents
- Personal security\*
- Environmental matters as listed at para 12 below

\* When a contract is located in an area where a genuine concern exists about employees 'off site' personal safety, the Safety Advisor/Manager is to carry out risk assessments to ensure that control measures are in place to identify and effectively mitigate these risks.

Control measures are to be clearly set out, including protection of the public.

### PROPOSED MANAGEMENT OF HEALTH AND SAFETY DURING THE CONSTRUCTION PHASE

We believe that the following proposals will help us to mitigate the risks as the work progresses:

#### 1. **TRAFFIC MOVEMENT**

- a) Wherever practical the layout of the site will include separate routes for vehicular traffic and pedestrians with priority given to safe access and egress to pedestrians. This principle will include for the elimination of reversing vehicles wherever possible. The traffic plan is to be made available to all suppliers and contractors working on site.
- b) Any existing fencing to the shared site boundary will be thoroughly examined to ensure that it conforms to HSG 151 and if not will be repaired or replaced accordingly
- c) Heras fencing may be required as a temporary measure and at these times will be 2 meters high with anti-climb mesh.
- d) Ply hoarding or heras fencing shall be used to fence off the site from the public.
- e) Construction activities audible beyond the boundary of the site should not be carried out than between the following times:
  - a. Monday-Friday 08.00am – 6.00pm
  - b. Saturday 8.00am – 1.00pm
- f) Overall working days, from site opening to site closing shall be between the hours of 07.00 – 18.00, allowing for operatives to arrive at work and leave after their working day. Audible activities will be as per the hours above.
- g) Delivery and removal of waste allowable times:
  - a. Monday-Friday 08.00am – 6.00pm
  - b. Saturday 8.00am – 1.00pm
- h) Wherever possible, deliveries between the hours of 8.30 – 9.00 and 15.00 – 15.30 shall be avoided as to not clash with local school drop offs and pick-ups. This shall be written into all subcontractor and supplier orders.
- i) Adequate signage will be displayed directing traffic to/from site and traffic movements into/out of site will be controlled by a trained banksman/ signaller.
- j) All deliveries will be either ridged or articulated Lorries via Arlesey Road.

- k) Audible warning devices will be fitted to vehicles that need to reverse, and they will be supervised by a banksman.
- l) A traffic layout plan is contained at the end of this section.
- m) Forklift trucks maybe required to travel on public highways. When doing so, they will not exceed 10mph and will use a fixed flashing beacon to warn members of the public of their presence.

## 2. **ACCESS TO/FROM SITE**

- a) Site traffic will be directed onto site via Arlesey Road.
- b) Vehicles arriving and/or exiting site will use the established routes designated with adequate signage. A one-way system, where practically possible, will be established to reduce the congestion of site traffic.
- c) Site vehicles will not be allowed to park outside the site, unless in emergency situations.
- d) Routes for ambulances and fire engines will be kept clear at all times.
- e) The access gates to the site will be securely locked outside normal working hours.
- f) A Pressure Washer shall be available at the main site entrance to clean off any vehicles requiring so before they exit the site. This shall be suitably drained upon the site.
- g) Site entrances, access roads and the adjacent public highway shall be kept clean using road sweeps, on an as and when required basis.
- h) Access to and from the site shall be made via the proposed traffic routes in Appendix IV. Signage shall be erected as per this plan ahead of commencement on site. These traffic plans shall be part of all contractor and material supplier order placed on the site. Any contractor / supplier found to have breached the proposed routes shall be notified at the earliest possible moment.

## 3. **UNDERGROUND SERVICES**

All necessary steps will be taken to accurately locate and identify existing underground services prior to any excavation taking place. These steps will include:

- a) Referral to all relevant statutory authority drawings.
- b) Communication with the relevant authorities in order to accurately locate services on site.

- c) Cable Avoidance Tool (CAT) and Genny surveys of all areas prior to excavation work.
- d) Issue of a Permit to Dig by the site manager.
- e) Where necessary a non-intrusive radar survey will be completed.

#### 4. **DUST, NOISE, DISTURBANCE**

- a) Most building operations are inherently noisy and/or dusty, but we will endeavour to keep these to a minimum by the use of sprays where applicable and by ensuring that all plant used on site has the appropriate silencers, baffles, etc.
- b) Dust should not present any great problems, but we will liaise with local representatives regarding any particularly noisy or dusty operations. When working close to the existing buildings temporary dust screens will be erected as required to ensure that dust contamination is kept to an absolute minimum. This will be monitored by the site manager and modified if required.
- c) Noise surveys will be carried out if and when conditions dictate and a copy of such surveys will be kept on site.
- d) Surplus materials will be placed in skips, for removal from site to a registered tip. All excavated material that is not required will be loaded onto suitable lorries and deposited of under licence. All demolition materials will be removed similarly.
- f) We will not allow any fires on site for the burning of materials.
- g) Site roads, site, entrance and adjacent public highways shall be regularly cleaned via a road sweep to keep all clean with additional visits as construction activities may require.
- h) Heras fencing to sensitive boundaries and watercourse protection shall be fitted with debris netting to aid with controlling dust on site.
- i) Work places shall be kept clean and tidy throughout the day and site checked in the afternoon of each day by the responsible site manager to ensure the development, site entrance and surrounding areas are clean and tidy at the end of each day.

## **5. MANUAL HANDLING**

- a) Designers have a duty under CDM to design out high-risk activities wherever possible, which should include the 'weight' implications of materials specified.
- b) Notwithstanding item 5 (a) above, all 'heavy' materials will be mechanically off-loaded and whenever possible transported around site by mechanical means, i.e. fork lift trucks, pallet trucks, sack trucks, wheelbarrows, etc.
- c) Where risks are identified then contractors will carry out written manual handling assessments, which will be prepared in accordance with Manual Handling Regulations. The assessments must be attached to the method statements.
- d) The manual handling of kerbs and slabs is not permitted and mechanical means will be used wherever practical. If mechanical means are not practical then a detailed risk assessment will be carried out.

## **6. PERMITS TO WORK**

Where necessary, the following permits will be issued by Hill:

- a) Permit to Work
- b) Permit to Enter (Confined Spaces)
- c) Hot Works
- d) Permit to Dig
- e) Permit to Lift

## **7. COSHH**

- a) Any necessary COSHH Assessments will be made by the relevant contractors and attached to their method statements.
- b) The site manager has overall responsibility to ensure that COSHH assessments are completed and to ensure that all relevant parties on site are aware of any operation that may affect other persons.

## **8. METHOD STATEMENTS, RISK ASSESSMENTS**

- a) All necessary Method Statements and Risk Assessments will be prepared and kept in separate method statement files, which are held on site.
- b) We work on the principle of 'He who creates the risk - creates the necessary Method Statement/Risk Assessment'.
- c) The requirement for a Method Statement will be highlighted to the sub-contractor by the Contracts Manager, at the pre-order meeting and the requirement thereof forms part of the contract documents.

- d) All such Method Statements/Risk Assessments must be available on site prior to that operation commencing. These will comply with the requirement of the Health and safety Policy to ensure that they are sufficient in detail and, if acceptable, will be signed on site by all operatives who will agree to comply with the Method statement/Risk assessment at all times. If at any stage of the work the Statement requires revision then work will not be permitted to continue until the revision is in writing and again all concerned have signed it.

## 9. **PERSONAL PROTECTIVE EQUIPMENT**

Any necessary Personal Protective Equipment (PPE) will be supplied by the relevant employer and must be worn as, when and where necessary. As a minimum, helmets, safety footwear and hi-viz clothing must be worn by all persons on site including visitors who must report to the site office on arrival.

## 10. **PROJECT SPECIFIC ACTIVITIES**

The following activities have been identified as containing significant risk and as such these activities will require detailed risk assessment and method statements:

- a) Demolition
- b) Asbestos Removal
- c) Excavations
- d) Contaminated Ground
- e) Falsework
- f) Steel Erection
- g) Scaffolding
- h) Roofwork
- i) Lifting Operations
- j) Confined Spaces
- k) Wall cladding
- l) Installing safety nets
- m) Hand Arm Vibration (HAV) \*
- n) Work at Height (WAH)
- o) WBV Whole Body Vibration
- p) Noise
- q) Environmental Matters

\* With regards to the above it is the responsibility of the contractor/sub-contractor to provide comprehensive methods and safe systems of work. They should, for example, provide details of all pneumatic tools vibration levels, exposure limits and the same tools noise levels. It is the principal contractor's duty to ensure these are provided.

## 11. PROTECTION OF THE PUBLIC

In addition to measures previously mentioned, the following actions are to be taken:

- a) Letter drops to close neighbours to keep informed of construction activities
- b) Meetings with concerned parties
- c) Talks to schools

## 12. ENVIRONMENTAL MATTERS

12.1 Construction projects generate many environmental matters that require control measures. To ensure that these matters are controlled the Environmental Tool box talks as listed below will be considered as 'Activities with Risk to Health and Safety' and will be part of the H&S Advisors/Managers inspections regime.

- a) Spill Controls
- b) Water Pollution Prevention (Fuel and Oils)
- c) Dust and Air Quality
- d) Noise and Vibration
- e) Water Pollution –SILT
- f) Water Pollution- Cement and Concrete
- g) Tree Protection
- h) Storage of Waste
- i) Storage and use of Petroleum, Diesel and Oils
- j) Bentonite
- k) Pumping and Over Pumping
- l) Washing down Plant and Machinery
- m) Be a Good Neighbour
- n) Working on Previously Developed Land

12.2 Where possible, materials gathered from the existing structures on site will be utilised later during the development of the site. This will predominantly be hardcore that shall be crushed and stockpiled on site for later use.

12.3 All surplus waste shall be removed from site through a licensed waste carrier to be segregated and recycled off site, targeting a 90% recycling rate.

12.4 Any hazardous materials found shall be separated and removed by licensed specialists in line with the contractor's own method statements and risk assessments.

12.5 The site has a watercourse running through the site. During demolition, where possible, a 10m exclusion zone shall be established, closer where existing buildings are closer to the watercourse. This shall be formed with herras fencing with debris netting to always protect the watercourse.

### **13. ECOLOGICAL MATTERS**

13.1 During demolition, guidance contained with the MKA Preliminary Ecological Appraisal and Preliminary Roost Assessment shall be followed.

13.2 The site has a watercourse running through the site. During demolition, where possible, a 10m exclusion zone shall be established, closer where existing buildings are closer to the watercourse. This shall be formed with herras fencing with debris netting to always protect the river habitat. This fencing is shown on the fencing plan in the appendix.

13.3 All trees and hedging shall be protected with tree protection fencing consisting of herras on feet with pegged stakes as shown on the fencing plan in the appendix.

13.4 Bat surveys shall be conducted before demolition work has commenced.

13.5 Light pollution from onsite demolition activities shall be kept to a minimum, with all machinery and welfare lighting turned off at night.

13.6 Retained grasslands to the riverbank and the south of the scheme (referenced G1 and G2) shall be fenced off with herras on feet with pegged stakes throughout the demolition phase as shown on the fencing plan in the appendix.

13.7 If demolition works occur outside of September – February, within bird nesting season, a bird nesting check by an experienced ornithologist shall be carried out before works commence to confirm the area is clear of nesting. If any is found this shall be protected with fencing until emptied.

13.8 An updated badger walkover will be undertaken before demolition commences.

13.9 A soil bund shall be installed between demolition works and in front of the herras fencing protecting the river, in all areas to add additional protection to the watercourse.

13.10 Where possible, excavations shall be covered at night to prevent animals becoming entrapped. If not possible then a scaffold board shall be left within the excavation as a ramp out. All excavations shall be checked each morning and prior to backfilling to ensure any trapped animals are removed.



Subject: Construction Management Plan

---

## Appendix I Site Fencing Plan







Subject: Construction Management Plan

---

## Appendix II On Site Traffic Management Plan



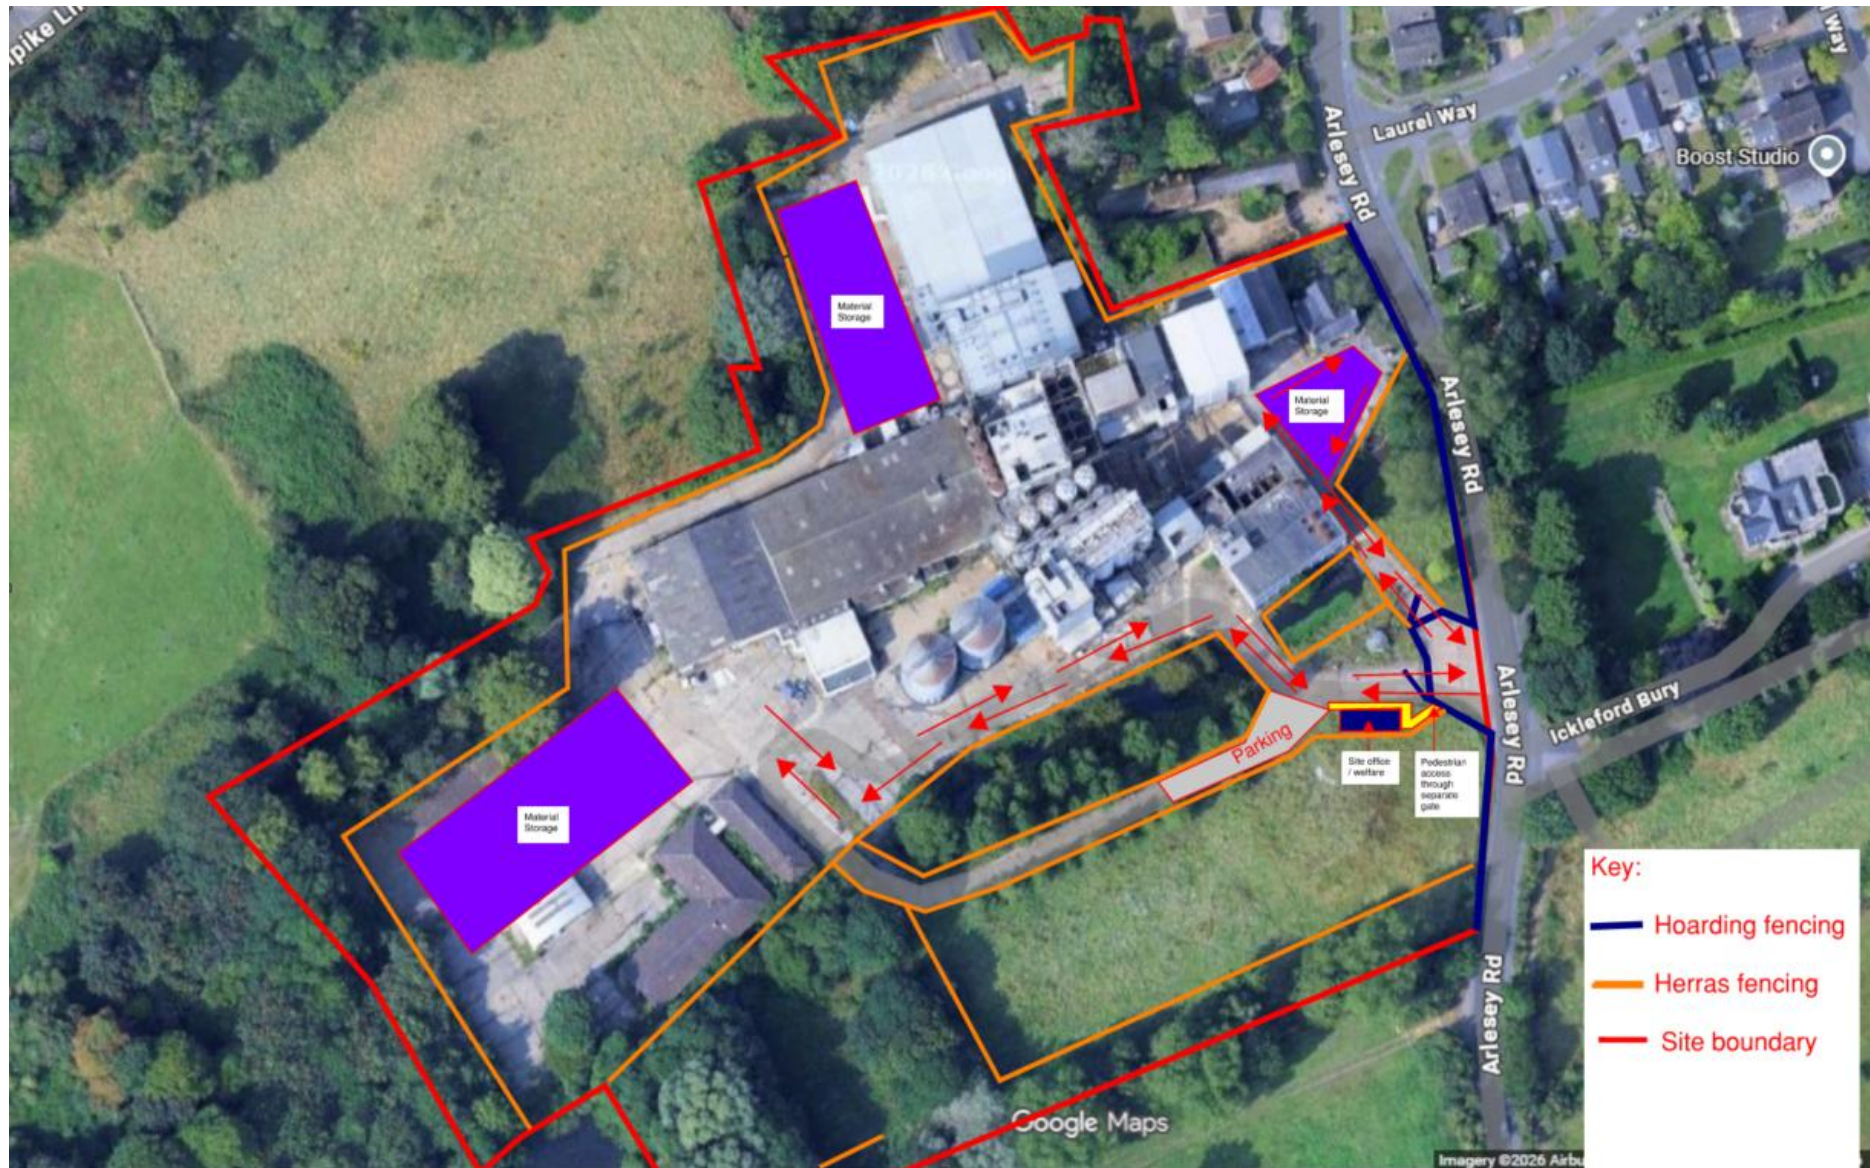


## Appendix III Demolition Site Set Up.

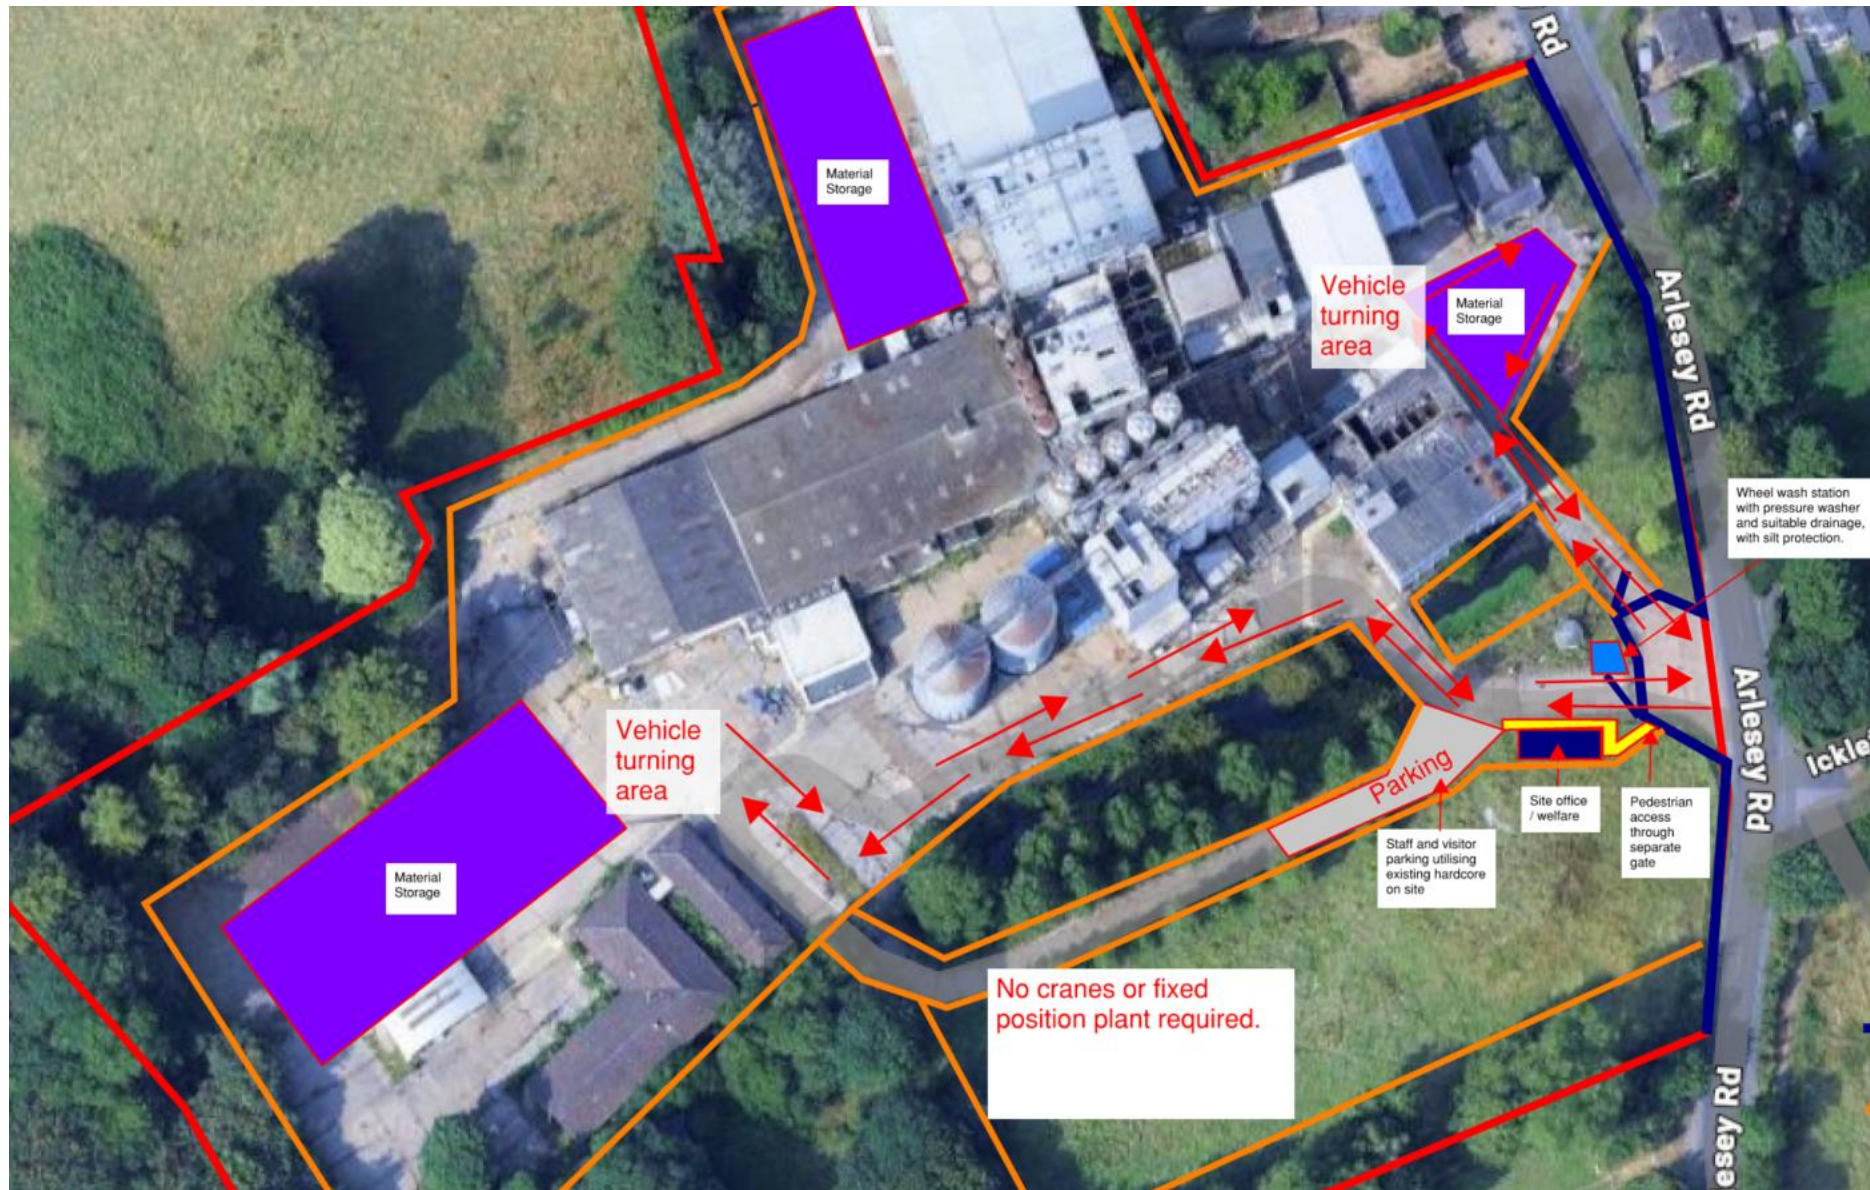

## Appendix IV Traffic Routes to Site


## Northern Routes to site

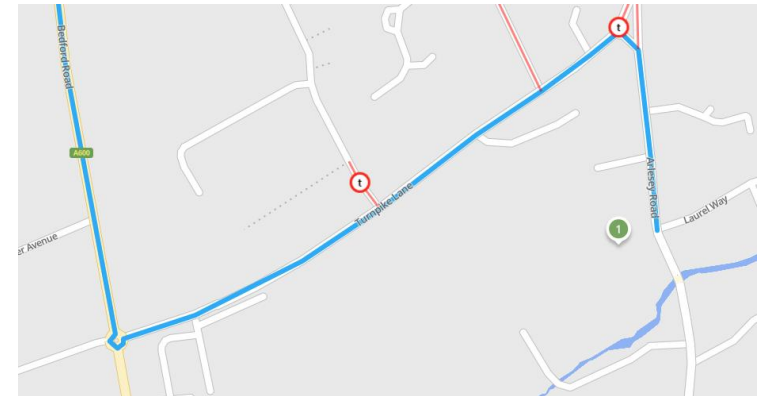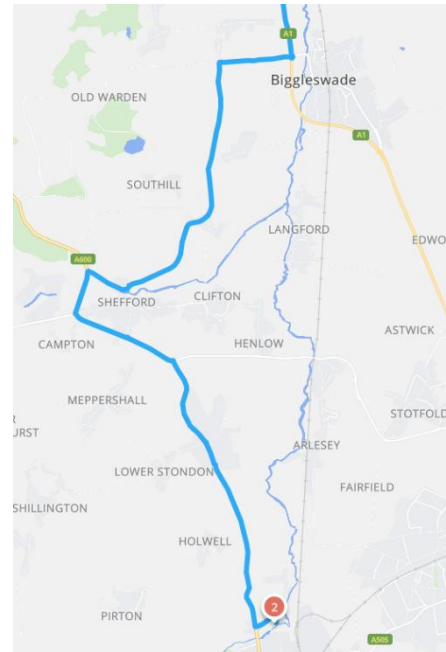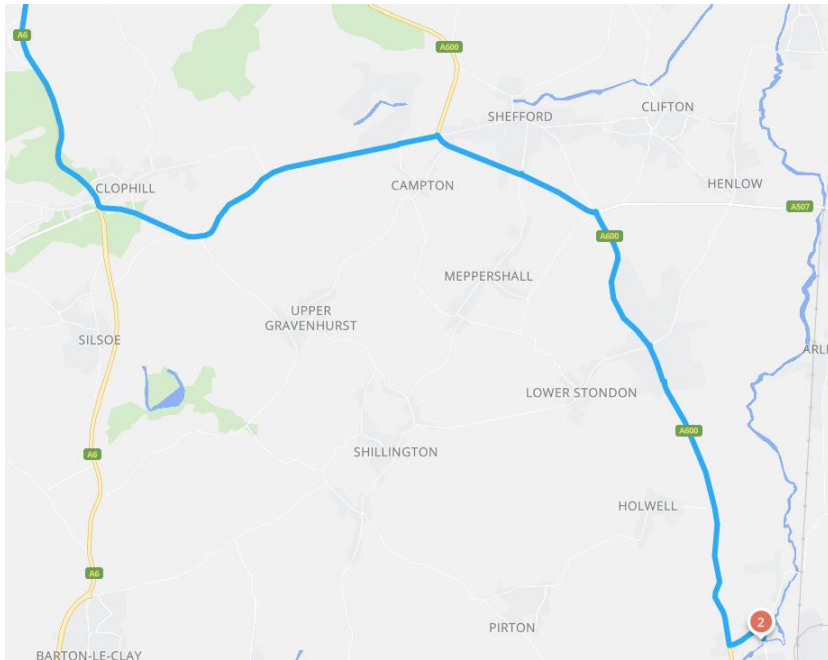

Northern routes to site via A1 / M1 to arrive via A600 from Shefford, turning left onto Turnpike Lane, right onto Arlesey Road, right into site. Yellow direction arrows to be located at Turnpike Lane and Arlesey Road Junctions. Caution site access ahead, vehicles turning signs to be located on Arlesey Road to North and South of site 50m from entrance.



## Southern Route to Site

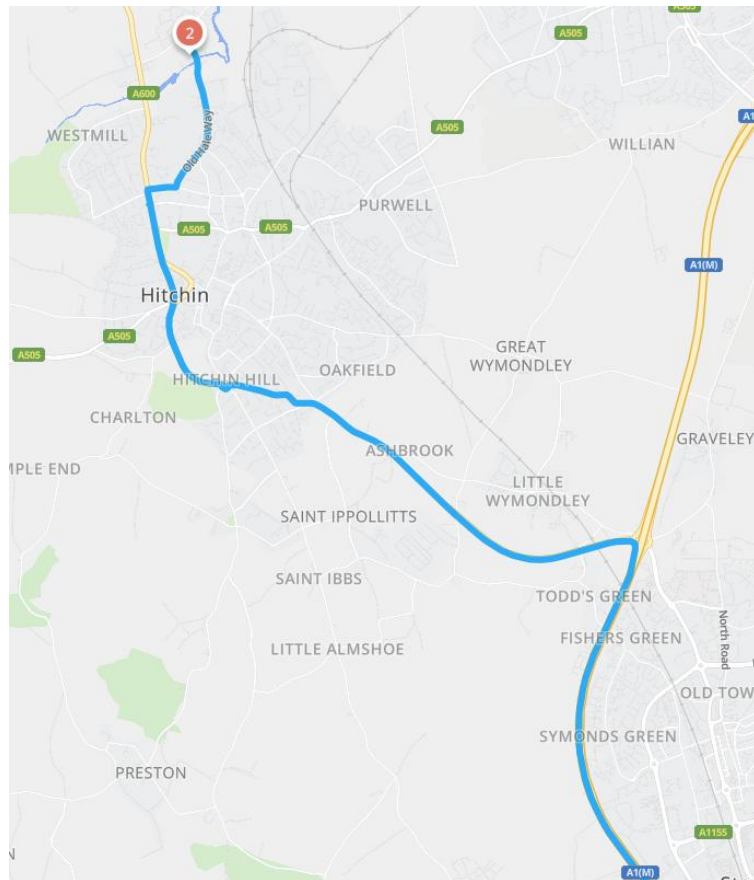


Southern route to site, off A1(M), slip road onto A602, through Hitchin via A602 onto Old Park Road, Bedford Road. Turning Right onto Bearton Road, left onto Old Hale Way leading to Arlesey Road. Turn left into site.

Yellow direction arrows to be located at Bearton Road and Old Hale Way Junctions. Caution site access ahead, vehicles turning signs to be located on Arlesey Road to North and South of site 50m from entrance.



## Western Route to Site

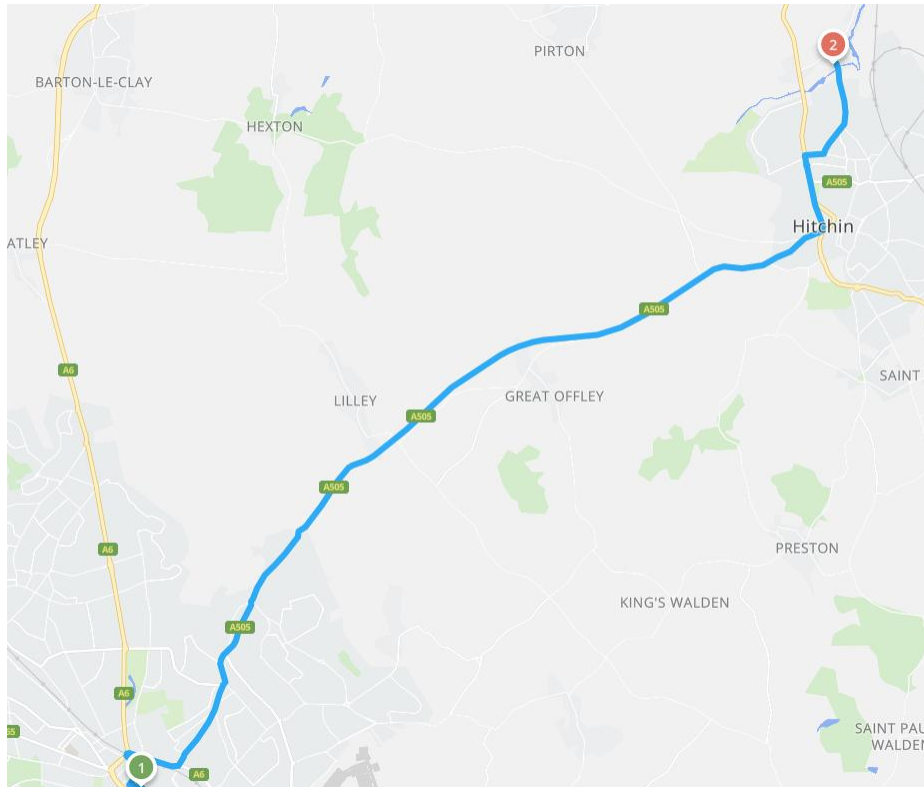

Western route to site, from Luton, along A505, turning left onto Old Park Road, Bedford Road. Turning Right onto Bearton Road, left onto Old Hale Way leading to Arlesey Road. Turn left into site.

Yellow direction arrows to be located at Bearton Road and Old Hale Way Junctions. Caution site access ahead, vehicles turning signs to be located on Arlesey Road to North and South of site 50m from entrance.



## Appendix V Enabling Works and Demolition Programme

Subject: Construction Management Plan

