

**ARBORICULTURAL IMPACT ASSESSMENT, PROTECTION PLAN AND
METHOD STATEMENT**

SITE:	GOSMORE ROAD, HITCHIN, SG4 9AN
SURVEY DATE:	13 AUGUST 2024
REPORT DATE:	18 DECEMBER 2024
OUR REFERENCE:	43-2009-7/15/2024
ON BEHALF OF:	Jon Read, Pentangle Design,
AUTHOR:	Mark Harrison, BSc (Hons), MarborA, NDArb




CONTENTS

1. INTRODUCTION	3
2. TERMS OF REFERENCE	3
3. DOCUMENTS SUPPLIED	6
4. PROTECTION STATUS	6
ARBORICULTURAL IMPACT ASSESSMENT.....	7
5. DEVELOPMENT / SITE APPRAISAL	7
6. TREE CATEGORISATION	7
7. DEVELOPMENT IMPLICATIONS.....	8
8. SERVICE RUNS	9
9. SITE PARKING, SITE HUTS, MIXING AND MATERIAL STORAGE AREAS.....	9
10. TREE PROTECTION.....	10
11. GROUND PROTECTION.....	12
12. CONSTRUCTION CONSIDERATIONS	13
13. SOFT LANDSCAPING WORKS	14
14. INSTALLATION OF BOUNDARY FENCES.....	14
9. POST DEVELOPMENT PRESSURES	15
ARBORICULTURAL METHOD STATEMENT (PRELIMINARY).....	17
10. METHOD AND PHASING OF WORKS	17
11. CONTACTS	18
12. DECLARATION	19
13. CONCLUSION	19
APPENDIX A – TREE SCHEDULE	20
APPENDIX B – GENERIC INFORMATION.....	27
APPENDIX C – BARRIER INFORMATION	29
REFERENCES	31
DIGITALLY APPENDED TREE PROTECTION PLAN (IN PDF FORMAT)	

ABBREVIATIONS

AIA	Arboricultural Impact Assessment	CMS	Construction Method Statement
AMS	Arboricultural Method Statement	RICS	Royal Institute of Chartered Surveyors
BRE	Building Research Establishment	RPA	Root Protection Area
BS	British Standard	TPBE	Trees and People in the Built Environment
CCS	Cellular Confinement System	TPO	Tree Preservation Order
CEZ	Construction Exclusion Zone	TPP	Tree Protection Plan



1. INTRODUCTION

- 1.1. Harrison Arboriculture Ltd. was commissioned to provide an arboricultural report to include an arboricultural impact assessment, tree protection plan and preliminary method statement for development proposals at Gosmore Road, Hitchin, SG4 9AN by Jon Read of Pentangle Design on behalf of Matthew Judge.
- 1.2. The site co-ordinates are 51°56'21.3"N 0°16'33.9"W which lies within the administrative area of North Hertfordshire District Council.

2. TERMS OF REFERENCE

- 2.1. To provide an assessment of the trees on and around the site regarding their suitability for retention within the context of the development based on the details provided. It assesses which of those will either have an impact on and/or be impacted upon by the development. The report includes methods by which those impacts can be mitigated if they are available and adheres to the recommendations provided in British Standard 5837:2012 'Trees in relation to design, demolition and construction - Recommendations' (BS 5837)
- 2.2. The report includes:

An Arboricultural Survey

The survey provides a plan indicating the size and positions of the trees on and close to the site. They are plotted and scaled based on the topographical survey provided by Survey Solutions, the final plan will be at 1:500 or larger as per RICS specification, it provides:

- Identification details and assessment of the current condition of trees within and close to the red line site.
- Recommendations for remedial works necessary and available to maintain their health and/or safety within the context of the development (for trees within the ownership of the applicants).
- Categorisation as per BS 5837 : 2012.

An Impact Assessment (AIA) / Constraints Plan

Based on the tree survey and proposed layout as illustrated by the Proposed Site



Plan reference 3707 06 provided by Pentangle Design The impact assessment provides:

- Details of tree loss and works (if any) required in implementing the proposed design.
- Identification of both above and below ground activities proposed in the vicinity of retained trees which may be potentially damaging e.g. removal of existing structures, the installation of hard surfacing, services installation and the location and dimensions of all proposed excavations or changes in ground level, including those necessary for the implementation of the recommended mitigation measures.
- The practicability of the scheme regarding access, adequate working space and provision for the storage of materials.
- Theoretical Root Protection Areas (RPA's) denoted as nominal circular areas centred on the trunk for all trees categorised A and B will be listed in the tree schedule.
- The RPA's for trees categorised C will be included in the tree schedule but will only be relevant where they are not under the ownership or management of the applicant or where they are to be retained within the development.

A Tree Protection Plan (TPP)

This will provide:

- Recommendations for the construction and positioning of suitable tree protection. It includes barrier fencing and both permanent and temporary ground protection where appropriate based on the AIA.
- The report will include possible methods to mitigate the adverse impacts of the development. The TPP illustrates the areas within or close to the RPA's within which measures are necessary to protect the root areas of retained trees.

Predicted impacts plan

- The predicted impacts are provided on plan reference 43-2009-7/15/2024



TPP and assess the expected impacts of the retained trees post development. The shade prediction is based on guidance provided by Building Research Establishment (BRE) in Site Layout Planning For Daylight and Sunlight - A guide to good practice.

An Arboricultural Method Statement

This will provide a precautionary approach appropriate to the proposals. It will describe the methods and sequence of tree protection that should be adopted in order to demonstrate that the operations can be undertaken with minimal risk of adverse impact on trees to be retained. It may require relevant information from other specialists. It will include some or all of the following:

- any operations proposed within the RPA (or crown spread where this is greater);
- removal of existing structures and hard surfacing;
- installation of temporary ground protection ;
- excavations and the requirement for specialised trenchless techniques ;
- installation of new hard surfacing including materials, design constraints and implications for levels;
- specialist foundations including installation techniques and the effect on finished floor levels and overall height;
- retaining structures to facilitate changes in ground levels;
- preparatory works for new landscaping;
- An auditable/audited system of arboricultural site monitoring, including a process by which adherence to the agreed methods and phasing within this report can be monitored;
- A schedule of specific site events requiring specialist arboricultural input or supervision; and
- A list of contact details for the relevant parties.



- 2.3. The scope and limitations of the report are listed in Appendix B – Generic Information.

3. DOCUMENTS SUPPLIED

Table 1 - Document summary

Document Title	Provided by	Reference
Location Plan	Pentangle Design	3707 01
Existing Site Plan	Pentangle Design	3707 02
Proposed Site Plan	Pentangle Design	3707 06F
Proposed Demolitions	Pentangle Design	3707 05A

4. PROTECTION STATUS

- 4.1. Trees subject to constraints such as Tree Preservation Orders and Conservation Areas are protected under the law. An online search at Harrison Arboriculture was not instructed to investigate whether trees on or adjacent to the site are protected. It is suggested that written confirmation from North Hertfordshire District Council is sought formally establishing the legal status of these trees prior to any works being undertaken outside the remit of an approved planning application.



ARBORICULTURAL IMPACT ASSESSMENT

5. DEVELOPMENT / SITE APPRAISAL

- 5.1. The site is residential property within landscaped gardens at Gosmore Road, Hitchin, SG4 9AN. It was surveyed on 4 August 2024.
- 5.2. The arboricultural survey has been amended to reflect trees 4, 10.4 and 10.5 lost in storms in November/December 2024.
- 5.3. The overall site is broadly flat with raised beds along the southern periphery.
- 5.4. The development proposal is for the removal of the existing building and the construction of three new residential units. The existing access is to be decommissioned and access proposed via a new entrance from Gosmore road.

6. TREE CATEGORISATION

- 6.1. The method of categorisation as provided by BS5837 can be found at Appendix A. The following is a summary of the trees present on the site and their grade (table 1). A and B category trees are a material consideration in the development process; the subcategories 1, 2 and 3 are intended to reflect arboricultural, landscape and cultural values respectively.

Table 2 - Tree Category Summary

C1	13		A	0
C2	0		B	0
C3	0		C	13
B1	0		U	0
B2	0		Total	13
B3	0			
A1	0		T	10
A2	0		G	3
A3	0		H	0



U	0	W	0
Total	13	Total	13

7. DEVELOPMENT IMPLICATIONS

- 7.1. The primary criterion, in Arboricultural terms, is the retention of as many appropriate trees as practicable, allowing development to proceed whilst providing them with space and protection both during and subsequent to the completion of the development. The following is an assessment of the likely impact of the development on trees which are worthy of retention and guidance on the type and extent of protection required to ensure their continued wellbeing within the proposed development and the future landscape.
- 7.2. Most tree roots are typically found in the upper 600mm of soil and any excavation or compaction of the ground within these areas has the potential to damage roots and impact the future health and potentially the stability of the trees.
- 7.3. Soil levels over tree root areas must be left largely unaltered and the soil structure maintained. The recommended root protection area is the theoretical space required sufficient to maintain tree health.
- 7.4. Trees 10.1 and 10.7 are U grade trees within group 10 in poor condition and would be recommended for removal despite the development.
- 7.5. The existing building, which is to be demolished, is a sufficient distance from the retained trees such that the barrier fence as described in section 10 and positioned as denoted on plan reference 43-2009-7/15/2024 TPP will provide sufficient protection during the demolition of the existing building.
- 7.6. The barrier fence must be installed prior to the start of the development (including demolition) to prevent vehicular movement and storage of materials over the root areas. Machinery to be used for the demolition is to be positioned outside the RPAs. No machine excavation is to be undertaken within the RPAs. Debris must not be stored over the root areas.
- 7.7. The proposed access lies over the RPAs of C grade trees 2 and 3. Which have been recommended for removal.



- 7.8. The detached garage for plot 3 lies over tree 10.9, part of group 10, tree 12 and tree 13 in addition to their canopies hanging low over the air space to be occupied by the garage. They will require pruning to allow its construction. They have been recommended for removal and mitigation provided as part of post development landscaping.
- 7.9. The remaining trees can be retained within the development proposals and protected for the duration of the project as described in section 10 and positioned as denoted on plan reference 43-2009-7/15/2024 TPP.

8. SERVICE RUNS

- 8.1. We have not been provided with details of underground services at this stage of the project.
- 8.2. Underground electricity, gas or foul and grey water services be required will require routing well outside the protection areas of trees which are to be retained. If the route is likely to pass close to or within the RPA's of the retained trees prohibitions on excavation within the RPA's applies. A specific method statement will be required describing the method to be used to minimise any root damage. These may potentially involve hand digging within the root areas and laying pipework between any significant roots or moling from a position outside the RPA's

9. SITE PARKING, SITE HUTS, MIXING AND MATERIAL STORAGE AREAS

- 9.1. All deliveries, material storage and contractor parking shall make use of the existing accesses and hard surfaces. Materials must not be stored within the root protection areas indicated by the CEZ as illustrated on plan reference 43-2009-7/15/2024 TPP and marked by barrier fence on site. If additional space is required for the storage and/or mixing of building materials within or close to the RPA's of the retained trees, sufficient ground protection must be installed to prevent soil compaction and/or contamination by any spillage.
- 9.2. Only the protected locations agreed can be used throughout both the ground work and the construction phases. If an alternative location is required, this must be




supported with a suitable protection plan and agreed in writing with North Hertfordshire District Council.

- 9.3. It is not known whether site huts are required for the site at this stage. If site huts are to be used they shall be sited away from the RPA's of retained trees. Site huts in close proximity to the existing tree protective barrier line which require siting on unsurfaced ground, shall have appropriate footings or be situated on a temporary surface. This is to reduce the potential for ground compaction. Site huts can be used as part of the protective barrier boundary, and in some cases, can be beneficial where installation does not conflict with the aerial parts of the tree.
- 9.4. If it is proposed that site huts, ground protection or stores are to be located within the RPA of retained trees for more than 3 months, a temporary irrigation and aeration system will be installed to ensure that the rooting environment is maintained in a good condition. The system will include a compressible layer of composted wood chip or forest bark over a geotextile separation layer, on which ground protection or site huts can be placed. Watering will depend on permeability of the soil, weather conditions and the extent of the area covered, but should include weekly watering from April to September, when no rainfall has occurred for more than four consecutive days.

10. TREE PROTECTION

- 10.1. Exclusion of construction activity from the unprotected recommended root protection areas from the outset will ensure those trees identified for retention are maintained in a safe and healthy condition preventing the following. They should be retained in place for the duration of the development to prevent:

- Root severance
- Damage to the bark, branches and trunks
- Compaction of the soil within the Construction Exclusion Zone
- Alterations in soil level
- Soil contamination by phytotoxic materials such as herbicides, petrol, oils, diesel, cement and concrete washings or other construction additives




Barrier Fence

- 10.2. Tree protection barriers will be erected prior to the construction process and shall remain in place until completion of the development. Signs will be attached informing all site staff that the area is to remain fenced, examples of signage can be found at the end of this document which can be laminated, or generic signs can be purchase on line.
- 10.3. The barrier fence in accordance with BS5837 2012 Section 6 Figure 3 (figure 1) is considered fit for purpose for this site given the size of the development and the degree of works taking place in proximity to the retained trees. The position of the Tree Protection Fencing is shown on the Tree Protection Plan reference is 43-2009-7/15/2024 TPP appended at the end of this document. This should be constructed with weld mesh panels, at least 2m high, securely fixed together with wire or scaffold clamps and braced with ground anchored supports at a maximum spacing of one every two Heras panels (every 6m) to brace the fence sufficiently to resist impacts. The BS figure has been reproduced at the end of this section. The fencing may also be securely attached to wooden posts a minimum size of 4 x 4 (100mm x 100mm) firmly driven into the ground.
- 10.4. Any adjustments or removals of the tree protection measures will only be carried out following consultation and agreement with the project arboriculturalist and/or the Local Authority tree officer.
- 10.5. The following shall apply to the areas within the tree protection area:
- No mechanical excavation and excavation by other means only with Arboricultural supervision
 - Hand digging shall only be carried out following a written method statement approved by the project arboriculturist
 - No adjustment to ground levels,
 - No storage of plant or material,
 - No storage or handling of any chemicals including cement washing,
 - No vehicular access,



- No fires.

Figure 1 - (BS5837 Figure 3) example of fence stabilization system

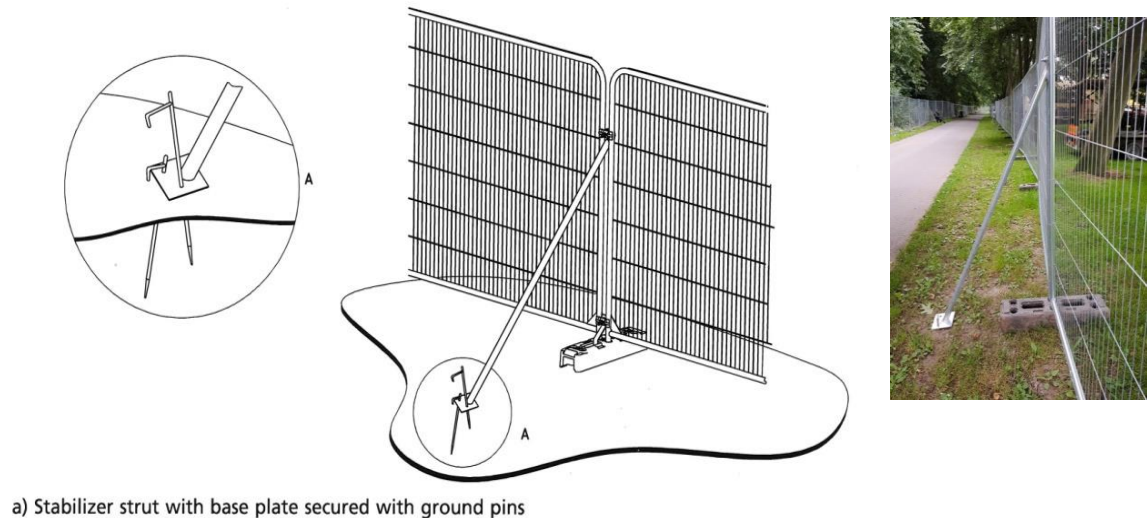

11. Ground Protection

- 11.1. Ground protection will be required where construction activity within or access across the RPA's is necessary. This is to prevent root damage and soil disturbance or compaction and is required for the duration of the development. This will be temporary where incursion is to facilitate the construction and permanent where traffic over the root area is required subsequent to the completion of the development.
- 11.2. Temporary ground protection is required to facilitate activity within the RPA's of tree no. 10.5. Permanent protection is not required for this site.

Temporary Ground Protection

- 11.3. The principle of ground protection is to spread the weight of anything using the area to prevent rutting or soil compaction and prevent any spillage leaching into the soil. It must be fit for purpose and designed to support the expected traffic. It should consist of a rigid surface layer over a compressible base (e.g. wood chip) laid over a separation membrane typically of geotextile.

The ground protection might comprise one of the following:

- a. for pedestrian movements only, a single thickness of scaffold boards placed either on top of a driven scaffold frame, so as to form a suspended*




walkway, or on top of a compression-resistant layer (e.g. 100 mm depth of woodchip), laid onto a geotextile membrane;

b. for pedestrian-operated plant up to a gross weight of 2 t, proprietary, inter-linked ground protection boards placed on top of a compression-resistant layer (e.g. 150 mm depth of woodchip), laid onto a geotextile membrane;

c. for wheeled or tracked construction traffic exceeding 2 t gross weight, an alternative system (e.g. proprietary systems or pre-cast reinforced concrete slabs) to an engineering specification designed in conjunction with arboricultural advice, to accommodate the likely loading to which it will be subjected. (British Standards Institute, 2015).

Figure 3: a. Diagrammatic illustration of ground protection within the RPA b. example of temporary ground protection.

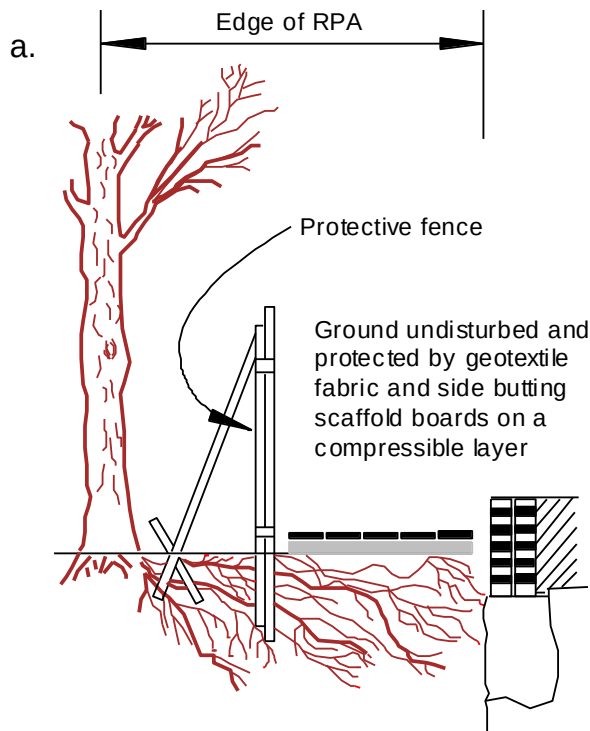


b.



12. Construction Considerations

12.1. The proposals are a sufficient distance from the retained trees that special construction considerations are not necessary.



13. SOFT LANDSCAPING WORKS

13.1. Any soft landscaping works within the development area should be in accordance with the approved landscape plan, and any specification of such works approved by the local planning authority which should adhere to the following British Standard Specifications and Codes of Practice:

- Trees should be supplied packaged in accordance with the recommendations of BS 3936:1992 Part 1 Nursery Stock - Specification for trees and shrubs;
- BS 4428:1989 - Code of Practice for General Landscaping Operations (excluding hard surfaces);
- BS 8545:2014 Trees from Nursery to Independence in the Landscape;
- The Code of Practice for Plant Handling 2002 (Horticultural Trades Association).

13.2. The construction exclusion zone will remain off limits for all site plant and machinery unless fit for purpose ground protection is installed. Pedestrian traffic must be kept to an absolute minimum only permitted for the ground preparation and landscape installation work.

13.3. The landscaping works will need to be undertaken in such a way as to avoid level changes, deep digging or mechanical rotovation. Excavation of planting pits within the RPA can cause serious harm the root system of retained trees. Planting pits within the RPA of retained trees will be excavated by hand to avoid damage to roots greater than 25mm and masses of smaller roots.

14. INSTALLATION OF BOUNDARY FENCES

14.1. Access within the CEZ for fence construction purposes can also result in soil compaction and deterioration of the soil structure. Concrete used to support the posts is poisonous to plants and which, if not controlled, can leach into the surrounding soil.



- 14.2. Fencing will need to be designed and constructed to minimise the need for excavation and allow minor variations of up to 300mm between post spacing to allow repositioning of posts where roots which are greater than 25mm are discovered during the excavation of postholes within the RPA of retained trees.
- 14.3. Postholes within the RPA should be excavated by hand and lined with heavy gauge polythene to prevent contamination of the rooting environment.
- 14.4. Fencing should be installed during period of dry weather so as to maintain soil structure and prevent compaction of the rooting environment.
- 14.5. Where significant traffic over the RPA's is required to install the boundary fence, fit for purpose ground protection will be placed along the line of construction to prevent compaction of the rooting environment of retained trees.
- 14.6. Where tree canopies hang low along the line of the proposed fence crown raising to facilitate construction may be required. This must be undertaken by an arboriculturist.
- 14.7. Bracing any part of the boundary fence from retained trees will not be permitted under any circumstances

15. POST DEVELOPMENT PRESSURES

Shading

The expected shading cast by the trees is based on guidance provided by Building Research Establishment (BRE) in Site Layout Planning for Daylight and Sunlight - A guide to good practice (BRE, 1991). The shade predictions are illustrated on the Tree Protection Plan reference 43/2009/7/15/2024 TPP appended at the end of this document.

Buildings.

Shade predictions are not expected to have an unreasonable impact on the availability of light to living space within the proposed dwellings.

Open spaces.

The shade cast by the retained trees is minimal both at their existing sizes and



future size and are not expected to have an unreasonable impact on the reasonable enjoyment of gardens.

Privacy and screening.

The screening provided by the existing trees and hedges can be maintained and new planting can be achieved to provide additional screening.

Direct damage.


There are no retained trees which are in such close proximity that would result in direct damage at their current size or resulting from future growth.

Seasonal nuisance.

The retained trees do not overhang the proposed building and leaf and debris fall is not expected to impact the dwelling over and above what can be considered typical for this type of setting.

Future pressure for removal.

The design of the site does not present any unreasonable impacts or pressures on future residents and no post development pressures for removal are expected.



ARBORICULTURAL METHOD STATEMENT (Preliminary)

16. METHOD AND PHASING OF WORKS

PRE - DEMOLITION / CONSTRUCTION

- 16.1. All permitted or approved tree work will be undertaken prior to the commencement of site preparation, demolition or construction works.
- 16.2. Tree work will be carried out in accordance with the British Standard *“Recommendations for Tree Work”* BS3998:2010, by suitably qualified and experienced professional arborists. Under no circumstances shall site personnel undertake any tree pruning operations.

Table 2 - Tree works summary.

Tree no	Species	Works required
10.1, 10.7	Prunus cerasifera (Cherry)	Remove
2 - 3	Acer pseudoplatanus (Sycamore) Prunus cerasifera (Cherry)	Remove
5	Fraxinus excelsior (Ash) Acer platanooides (Norway Maple)	Remove
12, 13	Fagus sylvatica (Beech) Prunus cerasifera (Cherry)	Remove

- 16.3. Prior to the start of any demolition or construction, including material storage, protective barrier will be erected as per BS5837 figure 3 as illustrated in section 10.
- 16.4. It will be positioned as denoted on the tree protection plan reference 43/2009/7/15/2024 TPP.
- 16.5. Signage informing all site workers that the area is to remain protected for the



duration of the development is to be attached to the fence. An example of signage can be found at the end of this document which can be printed, laminated and securely attached to the barrier fence if required.

- 16.6. The project arboriculturalist will be on hand to provide advice and/or supervision if required.

CONSTRUCTION

- 16.7. All barrier fence and ground protection is to remain serviceable and in position for the duration of the development. No adjustments are to be made unless with the written agreement of the planning/arboricultural officer.
- 16.8. Landscaping works may be necessary prior to the completion of the build. In this case prohibitions on traffic and movement over the Construction Exclusion Zones will remain in effect and activity will require additional fit for purpose temporary ground protection, no machine movements and the transport of materials into these areas will be made manually.
- 16.9. The project arboriculturalist will be on hand to provide arboricultural advice if it is needed.

POST CONSTRUCTION

- 16.10. Barrier fence and temporary ground protection is to be removed.
- 16.11. Site reinstatement and landscaping will be undertaken. Prohibitions on traffic and movement over the Construction Exclusion Zones will remain in effect and activity will require additional fit for purpose temporary ground protection, no machine movements and the transport of materials into these areas will be made manually.

17. CONTACTS

Organisation	Contact Name	Contact number	Email / online contact
Agent	Jon Read Pentangle Design,	01462 431133	
Harrison Arboriculture	Mark Harrison	07915 847 367	mark@harrisonarboriculture.co.uk



North Hertfordshire District Council	Case officer		
--	--------------	--	--

18. DECLARATION

- 18.1. The statements in this report are based on information provided by the client. It does not take into account, the effects of extremes of climate, vandalism or accident. Harrison Arboriculture cannot accept liability in connection with these factors, nor where prescribed work is not carried out in a correct and professional manner in accordance with current good practice.
- 18.2. The authority of this report is effective for two years from the date of the survey or when any site conditions change, or pruning or other works unspecified in the Report are carried out to, or affecting, the subject tree(s), whichever is the sooner. It is recommended that a new survey be carried out after twelve months or following any severe weather event or change in the site.

19. CONCLUSION

- The tree works are required both to facilitate the development as well as in the interest of maintaining industry standard.
- Landscaping to include tree planting could mitigate for the loss of trees on this site in the long term.
- Post development pressures for works on the retained trees are not expected as a result of the proposal.
- The proposed development would not have adverse impacts on the long-term vitality of the retained trees providing the methodology set out in this document are followed.



APPENDIX A – TREE SCHEDULE

Site: Gosmore Road, Hitchin, SG4 9AN

Date: 13 August 2024

* Recommendations are provided based on the initial survey independent of the proposal by default. Recommendations in italics within parentheses relate to works required to facilitate the development as identified by the impact assessment.

Tree no	Species	Height/m	Stem Diameter/mm (no. stems)	Age	Condition		Life Exp / yrs	Canopy Height/m				First Significant Branch Hgt/m	Canopy Spread/m				Comments	Recommendations	Category	Root protection	
					Physiological	Structural		N	E	S	W		N	E	S	W				Radius/m	Area/sqm
T1	Prunus cerasifera (Cherry)	4	180(1)	Mature	Fair	Fair	10+	2	2	2	2	1(N)	2	2	2	1.5	Previously crown reduced.	None required at time of inspection. <i>*(remove to facilitate the access)</i>	C1	2.16	14.66
T2	Acer pseudoplatanus (Sycamore)	8	220(1)	Early Mature	Fair	Fair	10+	2.5	2.5	2.5	2.5		2.5	2.5	2	2	Previously crown reduced. Basal/trunk suckers.	None required at time of inspection. <i>(remove to facilitate the access)</i>	C1	2.64	21.9
T3	Acer pseudoplatanus (Sycamore)	17	260,330,500(3)	Early Mature	Fair	Fair	10+	2.5	2.5	2.5	2.5		4.5	4	4.5	4.5	Previously crown reduced. Basal/trunk suckers.	None required at time of inspection. <i>(remove to facilitate the access)</i>	C1	7.84	193.12
-	Fraxinus excelsior (Ash)	10	290,200(2)	Early Mature	Fair	Fair	10+	3	1.5	3	5		4	4.5	2	3	Ash dieback. Previously crown reduced. Basal/trunk suckers. Foliage/bud density thin. Major dead wood >50mm.	LOST IN STORM 12-24	-	-	-
T5	Acer platanoides (Norway Maple)	12	440(3)	Early Mature	Fair	Fair	10+	3	1.5	3	5		3	4	3	4.5	Previously crown reduced. Minor dead wood <50mm.	None required at time of inspection. <i>(remove to facilitate plot 2)</i>	C1	9.14	262.48
T6	Acer platanoides (Norway Maple)	12	390(1)	Early Mature	Fair	Fair	10+	3	1.5	3	5		2.5	4	4.5	4.5	Previously crown reduced. Minor dead wood <50mm.	None required at time of inspection.	C1	4.68	68.82
T7	Acer pseudoplatanus (Sycamore)	9	140,100(2)	Early Mature	Fair	Fair	10+	3	1.5	3	5		1	2	2.5	2	Previously crown reduced. Suppressed. Minor dead wood <50mm.	None required at time of inspection.	C1	2.06	13.33
T8	Quercus robur (Pedunculate Oak)	25	840(1)	Mature	Fair	Fair	10+	15	15	12	20		8	10	8.5	9	Previously crown reduced. Suppressed. Minor dead wood <50mm.	None required at time of inspection.	B2	10.08	319.25
G9	Prunus cerasifera (Cherry)	5	150(5)	Early Mature	Fair	Fair	10+										Suppressed.	None required at time of inspection.	C1	4.02	50.78
G10	Prunus cerasifera (Cherry)	8-15		Mature	Fair	Fair	10+										Suppressed.	None required at time of inspection.	C1	Error	Error



Tree no	Species	Height/m	Stem Diameter/mm (no. stems)	Age	Condition		Life Exp / yrs	Canopy Height/m				First Significant Branch Hgt/m	Canopy Spread/m				Comments	Recommendations	Category	Root protection	
					Physiological	Structural		N	E	S	W		N	E	S	W				Radius/m	Area/sqm
10.1	Prunus cerasifera (Cherry)	6	310(1)	Mature	Poor	Poor	<10										Previously crown reduced. Suppressed. Decay in stem.	None required at time of inspection.	U	3.72	43.48
10.2	Prunus cerasifera (Cherry)	8	210,230(2)	Mature	Fair	Fair	10+	3					3	4.5	2	3	Previously crown reduced. Suppressed. Basal/trunk suckers. Decay in stem.	None required at time of inspection.	C1	3.73	43.71
10.3	Fraxinus excelsior (Ash)	8	330(1)	Mature	Fair	Fair	10+	3					2.5	1.5	2.5	3	Previously crown reduced.(on raised bed)	None required at time of inspection.	C1	3.96	49.27
-	Prunus cerasifera (Cherry)	8	290(1)	Mature	Fair	Fair	10+	2					3	3	2.5	1	Previously crown reduced. Suppressed. Narrow forks with included bark.	LOST IN STORM 12-24	-	-	-
-	Crataegus monogyna (Thorn)	10	300(1)	Mature	Fair	Fair	10+	4					2	1	1	1.5	Previously crown reduced. Suppressed. Narrow forks with included bark. Foliage/bud density thin.	LOST IN STORM 12-24	-	-	-
10.6	Prunus cerasifera (Cherry)	10	470(1)	Mature	Fair	Fair	10+	8					3	2	3.5	1.5	Previously crown reduced. Narrow forks with included bark.	None required at time of inspection.	C1	5.64	99.95
10.7	Prunus cerasifera (Cherry)	10	290(1)	Mature	Fair	Fair	10+	8					3	1	2	1	Previously crown reduced. Suppressed. Basal decay. Narrow forks with included bark.	None required at time of inspection.	U	3.48	38.05
10.8	Fraxinus excelsior (Ash)	5	170(1)	Early Mature	Fair	Fair	10+	3					1	1	1	1	Previously crown reduced. Suppressed.(on raised bed)	None required at time of inspection.	C1	2.04	13.08
10.9	Prunus cerasifera (Cherry)	10	470(1)	Mature	Fair	Fair	10+	2					3	3	2	2	Previously crown reduced. Fungal Brackets Present (Phelinus). Narrow forks with included bark.	None required at time of inspection.	C1	5.64	99.95
T12	Fagus sylvatica (Beech)	15	460(1)	Mature	Fair	Fair	10+	2					5.5	5	3	2.5	Crossing/rubbing stems. Narrow forks with included bark. Crossing/rubbing branches.	None required at time of inspection. (remove to facilitate plot 2 garage)	C1	5.52	95.74
T13	Prunus cerasifera (Cherry)	10	570(1)	Mature	Fair	Poor	<10	3					4.5	3	2.5	1.5	Previously crown reduced. Decay in stem. Fungal Brackets Present.	None required at time of inspection. (remove to facilitate plot 2 garage)	C1	6.84	147
T14	Acer pseudoplatanus (Sycamore)	15	600(2)	Early Mature	Fair	Fair	10+	4	4	4	5	2(W)	5	6	3	4	Off site. Diameter Estimated. Previously crown reduced. Suppressed. Minor dead wood <50mm.	None required at time of inspection.	C1	10.19	326.25



Tree no	Species	Height/m	Stem Diameter/mm (no. stems)	Age	Condition		Life Exp / yrs	Canopy Height/m				First Significant Branch Hgt/m	Canopy Spread/m				Comments	Recommendations	Category	Root protection	
					Physiological	Structural		N	E	S	W		N	E	S	W				Radius/m	Area/sqm
G15	Corylus avellana (Hazel),Crataegus monogyna (Thorn),Prunus cerasifera (Cherry),Tilia tomentosa (Lime)	10	600(4)	Early Mature	Fair	Fair	10+											None required at time of inspection.	C1	14.4	651.53
15.1	Crataegus monogyna (Thorn)	5	180(1)	Early Mature	Fair	Fair	10+						1	1	1	1			C1	2.16	14.66
15.2	Corylus avellana (Hazel)	5	100(5)	Early Mature	Fair	Fair	10+						1	1	1	1			C1	2.69	22.74
15.3	Prunus cerasifera (Cherry)	8	180(1)	Early Mature	Fair	Fair	10+						1	1	1	1			C1	2.16	14.66
15.4	Tilia tomentosa (Lime)	9	150(1)	Early Mature	Fair	Fair	10+						1	1	1	1			C1	1.8	10.18
15.5	Prunus cerasifera (Cherry)	8	200(1)	Early Mature	Fair	Fair	10+						1	1	1	1	Basal/trunk suckers.		C1	2.4	18.1



Key

1. Tree Ref No:

This relates to the numbers on the plan. Where trees have been tagged, the tag number will be used as the tree reference number. Individual trees are not prefixed and prefixed with a G, W or H represent a group, woodland or hedge respectively.

2. Species:

The name given is the Latin name by default. Where common names are given they are shown in parentheses.

3. DBH (Diameter at breast height):

This is the stem diameter at 1.5 metres (breast height) above ground level, given in millimetres. Where trees are multi-stemmed trees the square root of the combined stem diameter is calculated.

4. H (Height):

The height of the tree measured where possible or estimated and recorded in metres.

5. Canopy Spread (Crown radius):

The average crown spread taken from the centre of the trunk to the tips of the live lateral branches given in metres. Measurements following the compass points North, East, South and West.

6. Canopy height:

Ave - Average Crown Height Clearance: (HaB Height above ground) — ground clearance of the canopy for each cardinal point given in metres.

7. First significant branch

The height of the first significant branch the direction of which is shown in parentheses.

8. Age:

Age assessment is based on growth stages rather than actual age in years and are recorded as follows

Y Young



SM Semi Mature – having reached up to 1/3 life expectancy

EM Early mature - having reached 1/3 of the expected life expectancy and is transitioning into maturity.

M Mature - over 2/3 life expectancy

OM Over-mature - fully mature, past peak condition and beginning to decline

V Veteran - trees of interest biologically, aesthetically or culturally because of significant age.

9. Condition

Physiological – Assessment of the overall health and vigour of the tree compared to what would normally be considered typical of a healthy tree of the species.

Condition categories are given as good, fair, poor or dead.

Structural – Assessment of the structural stability of the tree based on visible signs of decay, damage, genetic weaknesses or faults. Structural categories are given as good, fair, poor or dead

10. Life Expectancy:

An estimate of the potential worthwhile remaining contribution – future life expectancy of the tree(s) in the present setting given normal circumstances, given in years (< = less than > = greater than) categorised <10 years, 10 – 20 years, 20 – 40 years and > 40 years.

11. Category:

A quality assessment of the trees based on criteria detailed in BS5837:2012 Table 1

U: Trees unsuitable for retention

A: Those of high quality and value

B: Those of moderate quality and value

C: Those of low quality and value

Assessments are based on their condition on the day of inspection and cannot account for future changes in circumstances.

12. Recommendations:

Preliminary management recommendations in relation to the proposed



development are made where appropriate. These may include remedial tree works that are deemed necessary to improve the quality of the tree or for safety reasons. Recommended tree works will be required to be in accordance with British Standard 3998:2010 Tree Work.

13. Root Protection

Radius – nominal circle centred at the stem centre providing the recommended radius of a circular area necessary for the continue wellbeing of the tree based on recommendations provided in British Standard 5837:2012

Area – The area necessary for the continue wellbeing of the tree based on recommendations provided in British Standard 5837:2012



Table 1

Category and definition	Criteria			Identification on plan
Category U Those in such a condition that cannot realistically be retained as living trees in the context of the current land use for longer than 10 years	• Trees that have a serious, irremediable, structural defect, such that their early loss is expected due to collapse, including those that will become unviable after removal of other category U trees (e.g. where, for whatever reason, the loss of companion shelter cannot be mitigated by pruning) • Trees that are dead or are showing signs of significant, immediate, and irreversible overall decline • Trees infected with pathogens of significance to the health and/or safety of other trees nearby or very low quality trees suppressing adjacent trees of better quality <i>NOTE Category U trees can have existing or potential conservation value which it might be desirable to preserve</i>			DARK RED
TREES TO BE CONSIDERED FOR RETENTION				
Category and definition	Criteria — Subcategories			Identification on plan
	1 Mainly arboricultural values	2 Mainly landscape values	3 Mainly cultural values, including conservation	
Category A Tree of high quality with an estimated remaining life expectancy of at least 40 years	Trees that are particularly good examples of their species, especially if rare or unusual, or essential components of groups, or of formal or semi-formal arboricultural features (e.g. the dominant and/or principal trees within an avenue)	Trees, groups or woodlands of particular visual importance as arboricultural and/or landscape features	Trees, groups or woodlands of significant conservation, historical, commemorative or other value (e.g. veteran trees or wood-pasture)	LIGHT GREEN
Category B. Trees of moderate quality with an estimated remaining life expectancy of at least 20 years	Trees that might be included in category A, but are downgraded because of impaired condition (e.g. presence of remediable defects including unsympathetic past management and minor storm damage) such that they are unlikely to be suitable for retention beyond 40 years; of trees lacking the special quality necessary to merit A categorisation	Trees present in numbers, usually as groups or woodlands, such that they form distinct landscape features, thereby attracting a higher collective rating than they might as individuals but which are not, individually, essential components of formal or semi-formal arboricultural features (e.g. trees of moderate quality within an avenue that includes better, A category specimens), or trees situated mainly internally to the site, therefore individually having little visual impact on the wider locality	Trees with material conservation or other cultural benefits	MID BLUE
Category C. Trees of low quality with an estimated life expectancy of at least 10 years, or younger trees with a stem diameter below 150 mm	Unremarkable trees of very limited merit or such impaired condition that they do not qualify in higher categories	Trees present in groups or woodlands, but without this conferring on them significantly greater landscape value, and/or trees offering low or only temporary screening benefit	Trees with very limited conservation or other cultural benefits	GREY
	NOTE Whilst C category trees will usually not be retained where they would impose a significant constraint on development, young trees with a stem diameter of less than 150 mm should be considered for relocation			



Appendix B – Generic information

TREE SURVEY

Scope and Limitations of Survey

1. This survey and report are concerned with the arboricultural aspects of the site only.
2. Only trees of significant stature were surveyed. Trees with a stem diameter of less than 75mm when measured at 1.5m above ground level (DBH) have been excluded unless they have particular merit that warrants comment.
3. The survey is restricted to trees that will be affected by the development within and adjacent to the site in accordance with guidelines detailed in British Standard 5837:2012 and with good practice as promoted by the Arboricultural Association and Arboricultural and Forestry Advisory Group (AFAG).
4. This survey is based on a ground level tree assessment and examination of external features only — described as the 'Visual Tree Assessment' (Mattheck and Breloer, The Body Language of Trees, DoE booklet Research for Amenity Trees No. 4, 1994). Although the structural conditions of the trees are considered and remedial action may be recommended it does not constitute a comprehensive Health and Safety report and if one is required it should be commissioned separately. No tissue samples were taken or internal investigations carried out.
5. No soil samples were taken or soil analyses carried out and the risk of tree-related subsidence to structures has not been assessed.
6. Consideration should be given to the timing of the proposed tree works to avoid the active growing period of trees. Tree work should ideally be carried out during the dormant period from November through to February and then again from June to August.
7. Although considered and wildlife habitat potential highlighted, no specific wildlife assessment has been carried out. It should be noted that The Wildlife and Countryside Act 1981, as amended by the Countryside Rights of Way Act 2000 and Conservation - Natural Habitats -Regulations 1994 provides statutory



protection to birds, bats and other species that inhabit trees.

8. This report should be read in conjunction with the Tree Protection Plan. The position of all trees and existing or proposed features are based on the plans provided by the client or other instructed professionals. Where trees have been omitted from the plans provided their position has been estimated or where possible plotted by triangulation.

Survey Method

1. In order to provide a systematic and consistent evaluation of the trees situated on the site, the following methodology was used in accordance with BS 5837: 2012.
2. The stem diameters of single stemmed trees were measured in millimetres at 1.5m above ground level (DBH). Multi-stemmed trees were measured at 1.5m above ground level and the RPA arrived at as per section 4.6a BS 5837:2012.
3. The height of visible trees was measured using a clinometer and estimated visually where view to the upper canopy obstructed.
4. The crown radii were measured where possible or estimated where access is restricted and are given for each cardinal point.
5. Where access to trees was obstructed or obscured, dimensions have been estimated.
6. Each tree has been assessed in terms of its arboricultural, landscape, cultural and conservation values in accordance with BS 5837: 2012 which are detailed in the Tree Schedule.



CONSTRUCTION EXCLUSION ZONE

BARRIER FENCE MUST NOT BE MOVED

**THE FOLLOWING IS PROHIBITED WITHIN THE
PROTECTED AREA**

No excavation, mechanical or otherwise

No adjustment to ground levels

No storage of plant or material

No storage or handling of any chemicals

No vehicular access

No fires




Additional examples of suitable signage






REFERENCES

- BRE. (1991). *Site Layout Planning For Daylight and Sunlight - A guide to good practice*. Construction Research Communications Ltd.
- British Standards Institute. (2015). Surveying for Bats in Trees and Woodland. *BS 8596*. British Standards Institute.
- Countryside Rights of Way Act . (2000). London: HMSO.
- H., M. C. (1994). *The body language of trees, Research for Amenity Trees no. 4*. HMSO.
- K. Rogers, V. L. (2014). Trees and People in the Built Environment II. *Determining Tree Growth in the Urban Forest*, (p. 84).
- Lonsdale, D. (2001). *Principles of Tree Hazard Assessment and Management*. London: HMSO.
- Rogers et al. (2014). TPBE II paper - Determining tree growth in the urban forest. Institute of Chartered Foresters.
- Technical Committee B/213, Trees and tree work. (2010). *Tree work - Recommendations*. London: BSI Standards Limited.
- Technical Committee B/213, Trees and tree work. (2012). *Trees in relation to design, demolition and construction - Recommendations*. London: BSI Standards Limited.
- Wildlife and Countryside Act. (1981). London: HMSO.

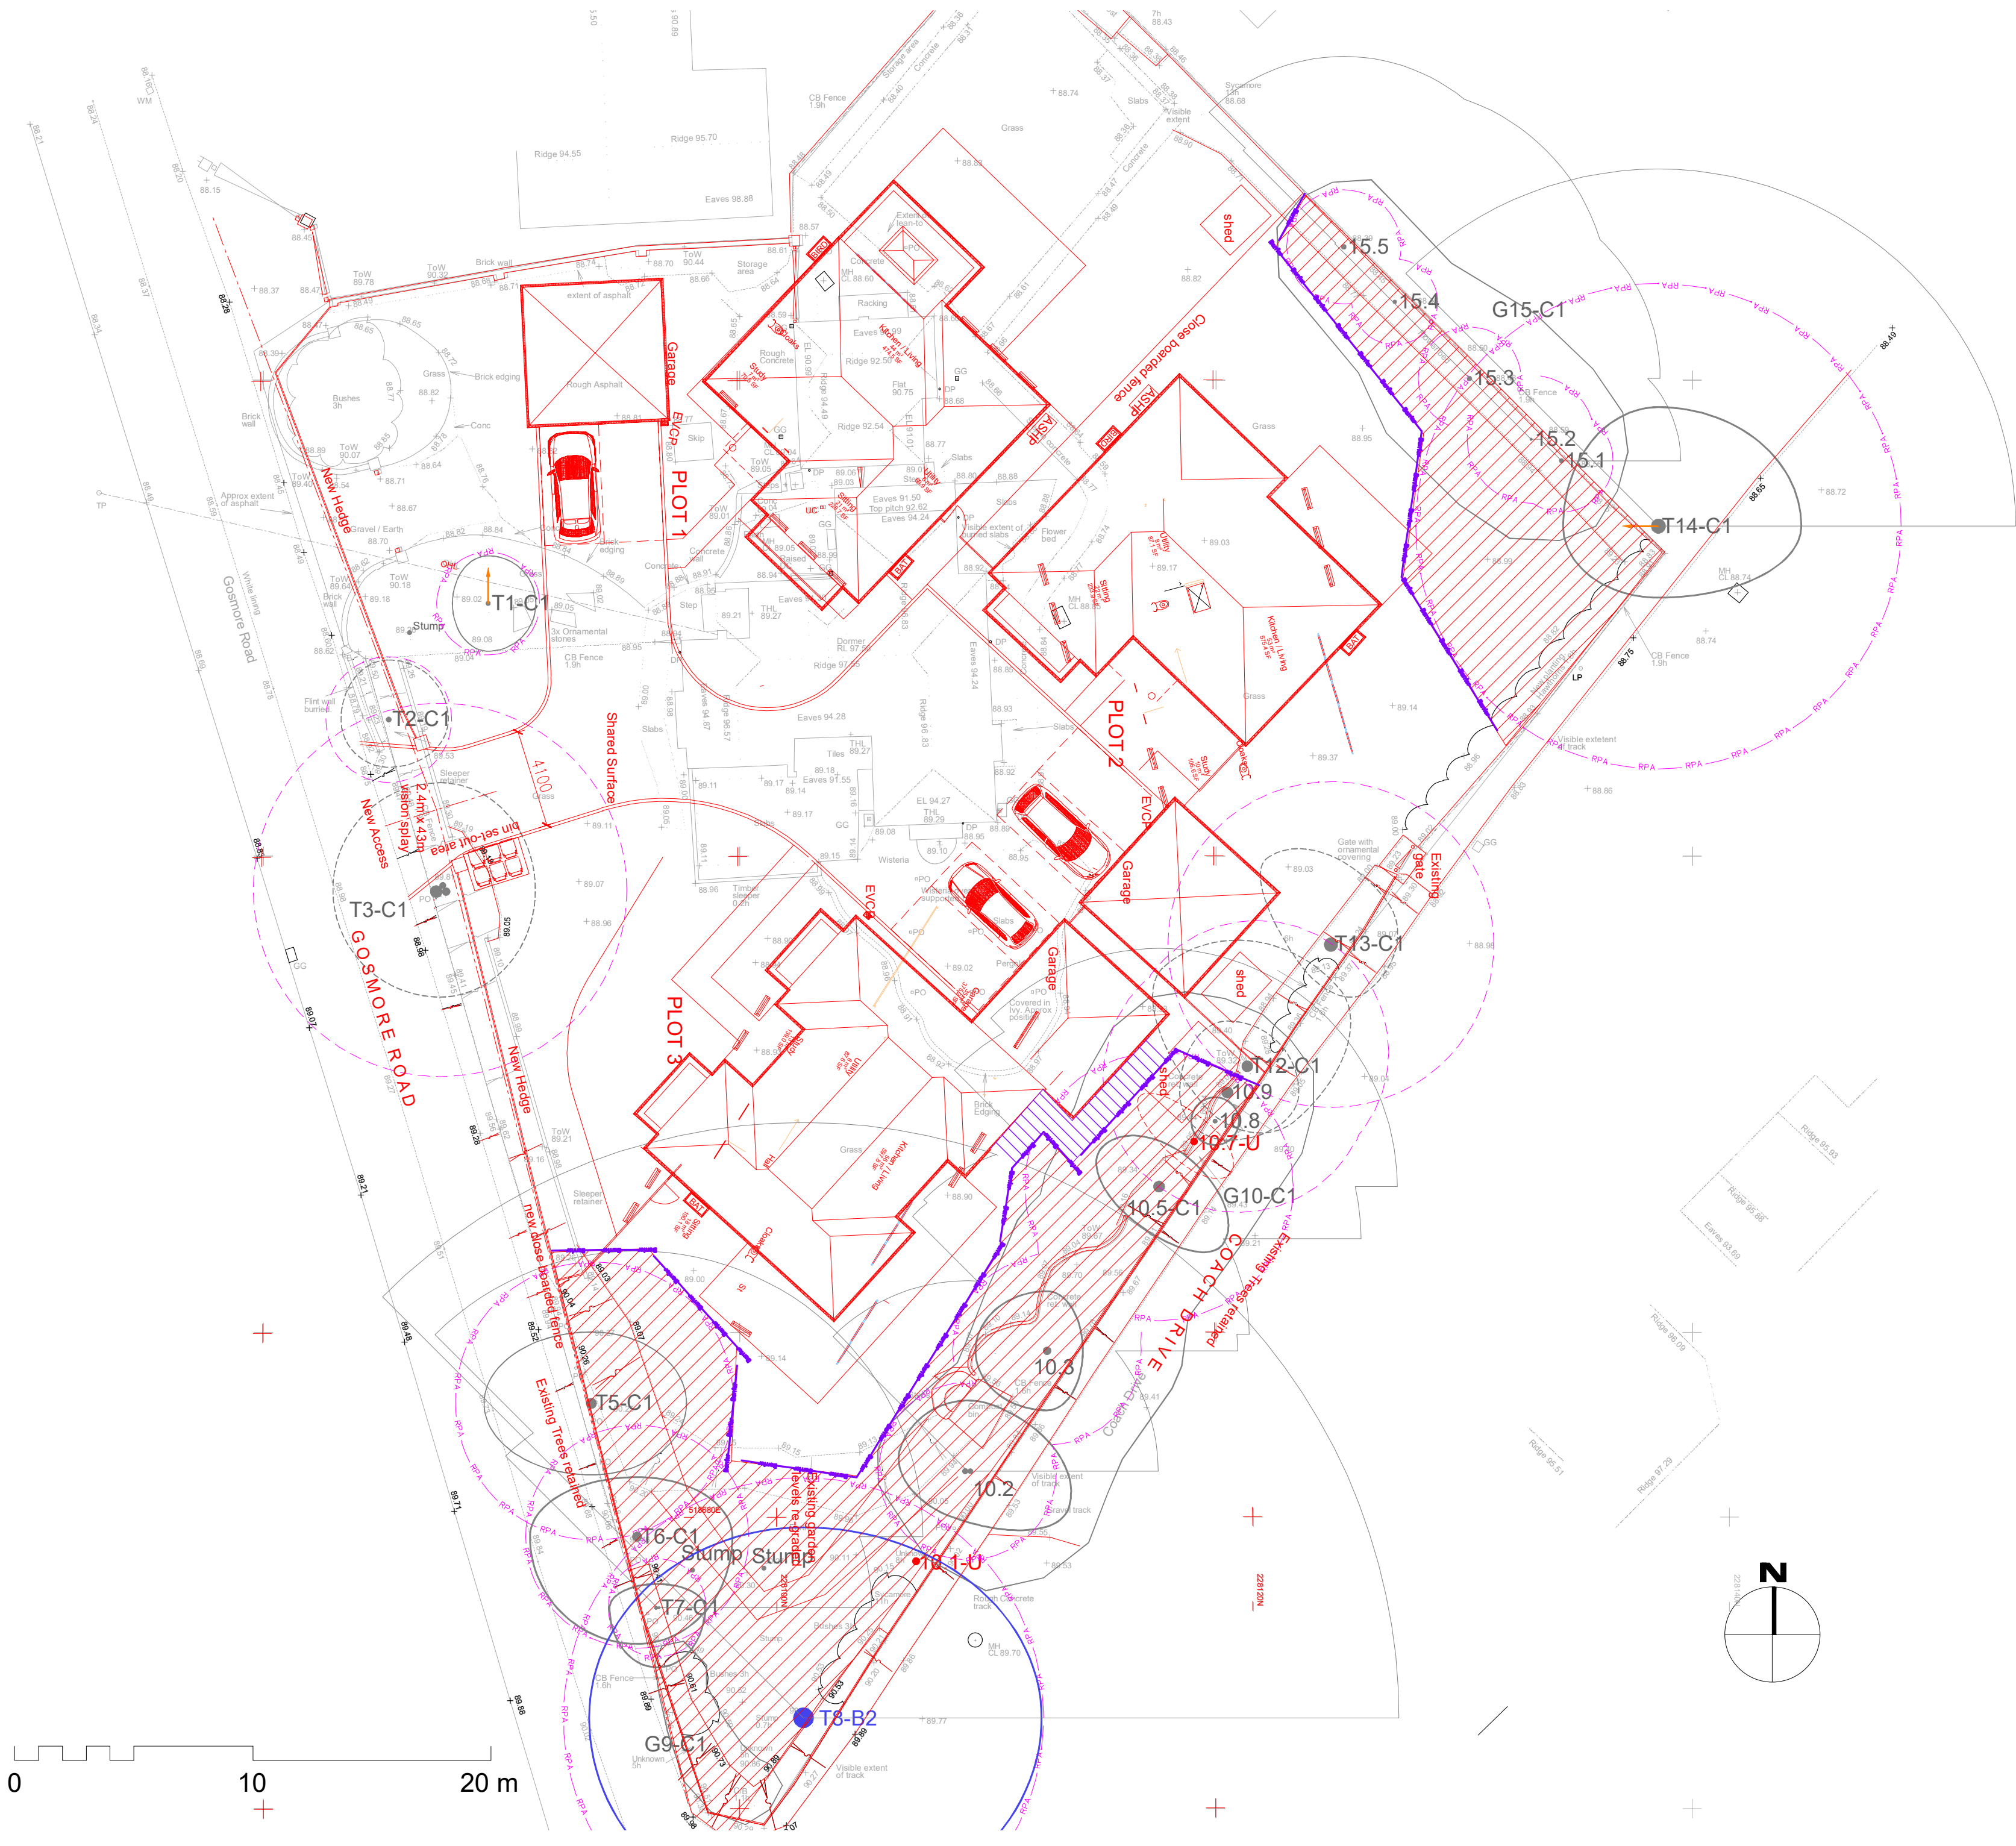

- Legend**
- Category A trees - Trees of high quality and value such that they make a substantial existing and future contribution for an expected 40 years or more.
 - Category B trees - Trees of moderate quality and value such that they make a significant future contribution for an expected 20 years or more.
 - Category C trees - Trees of low quality and value which might be expected to remain for around 10 years or less or with stems of less than 150 mm diameter.
 - Category U trees - Trees of low quality and value which are considered to have little or no potential due to disease or defects.
 - Number suffixes relate to the subcategories 1, 2 and 3 which are intended to reflect arboricultural, landscape and cultural values respectively
 - Direction of the first significant branch
 - The root protection area is the theoretical area considered necessary to provide sufficient room for the root growth required to support the tree - activity impacting the soil should be avoided.
 - The construction exclusion zone (CEZ) is the area within the root protection area. Access into this area should be prohibited for the duration of the project unless suitably protected to prevent any construction activities including storage.
 - Barrier fence to be installed as per BS5837, section 6, Figure 3.

Figure 3 BS 5837 : 2012 - Default Specification for Protective Barrier



- Material storage and mixing to be confined to these areas.
- Permanent ground protection provides protection to roots and underlying soil within the RPA's of retained trees during and subsequent to the development.
- The shade prediction is based on guidance provided by Building Research Establishment (BRE) in Site Layout Planning for Daylight and Sunlight - A guide to good practice (BRE, 1991)
- Trees to be removed to facilitate the development (dashed line of category colour)
- Temporary ground protection provides protection to roots and underlying soil within the RPA's of retained trees during the development to provide work space.
- Proposals

CLIENT	Pentangle Design									
SITE	GOSMORE ROAD, HITCHIN, SG4 9AN									
DRAWING	Title	Tree Protection Plan								
	Version	2			Revision	A				
	Base plan ref.	3707 06 Proposed Site Plan								
DRAWING NO.	43-2009-7/15/2024 TPP									
SCALE	1:200 @ A2									
DATE	18 December 2024									
DRAWN BY	M.Harrison									
