Dynamic Cone Penetration Test (DCPT) for Subgrade Assessment

Project No: 72302
Site: Royston
Test Location: DCP1
Date: 24/06/2014

Title	DCP1				
start (mm bgl)	finish (mm bgl)	start	finish	DCP Blows	CBR %
0	100	0	5	5	13
100	200	5	11	6	16
200	300	11	22	11	30
300	400	22	32	10	25
400	500	32	49	17	48
500	600	49	62	13	40
600	700	62	72	10	25

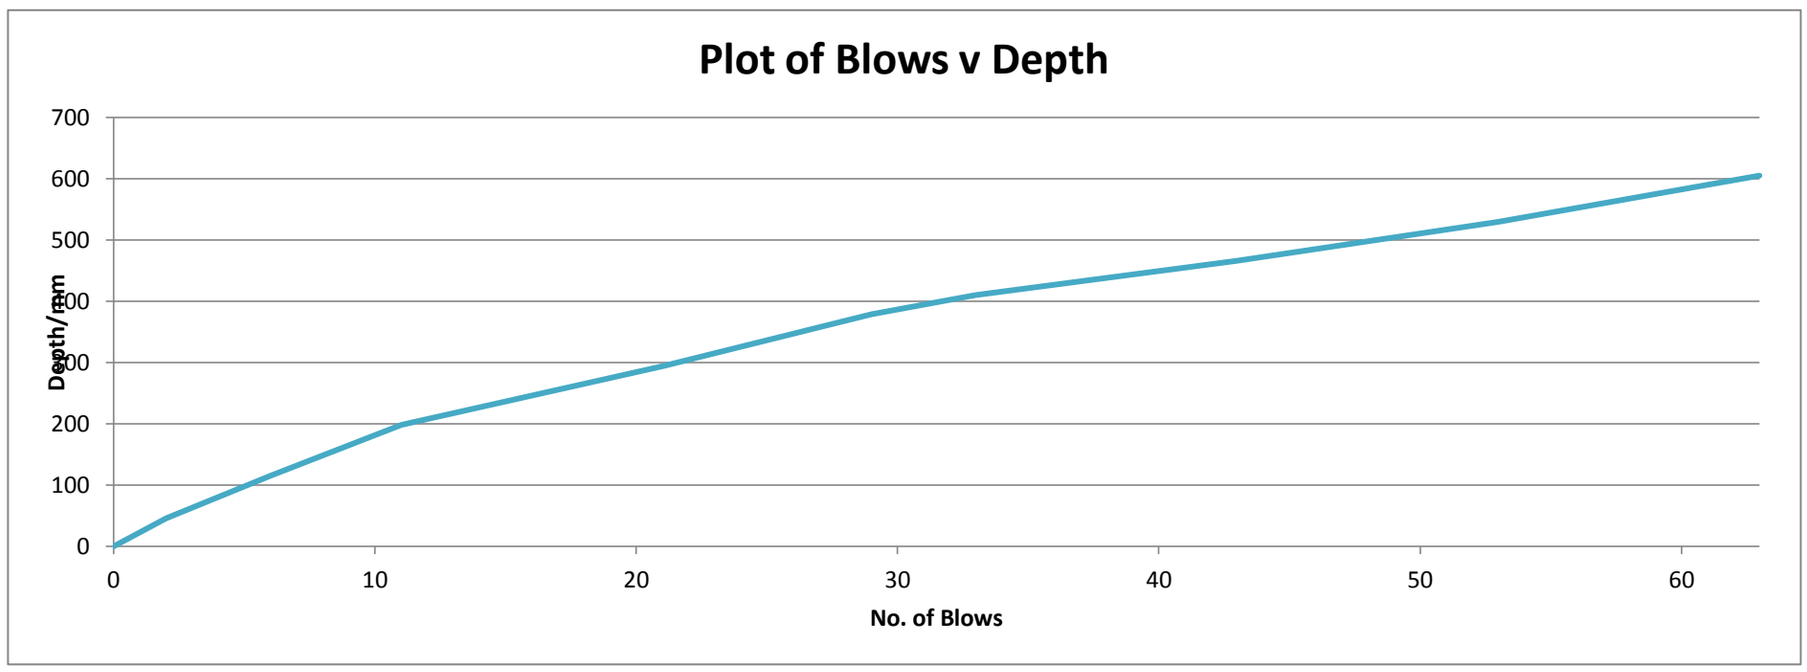

Dynamic Cone Penetration Test (DCPT) for Subgrade Assessment

Project No: 72302
Site: Royston
Test Location: DCP2
Date: 24/06/2014

Title	DCP2				
start (mm bgl)	finish (mm bgl)	start	finish	DCP Blows	CBR %
0	100	0	4	4	10
100	200	4	10	6	16
200	300	10	35	25	60
300	400	35	93	58	60

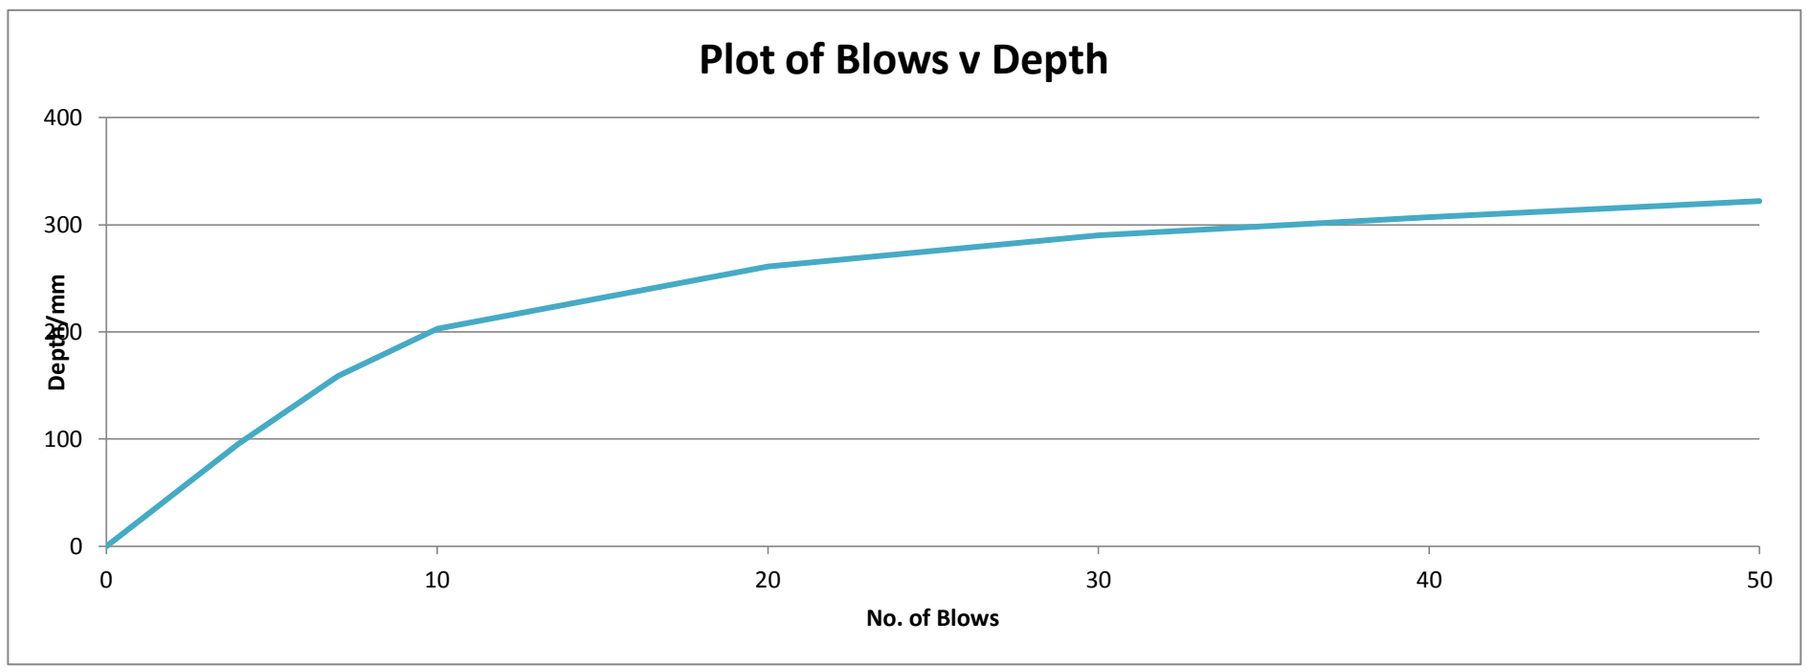

Dynamic Cone Penetration Test (DCPT) for Subgrade Assessment

Project No: 72302
Site: Royston
Test Location: DCP3
Date: 24/06/2014

Title	DCP3				
start (mm bgl)	**finish (mm bgl)**	**start**	**finish**	**DCP Blows**	**CBR %**
0	100	0	4	4	10
100	200	4	10	6	16
200	300	10	20	10	25
300	400	20	50	30	60
400	500	50	75	25	60

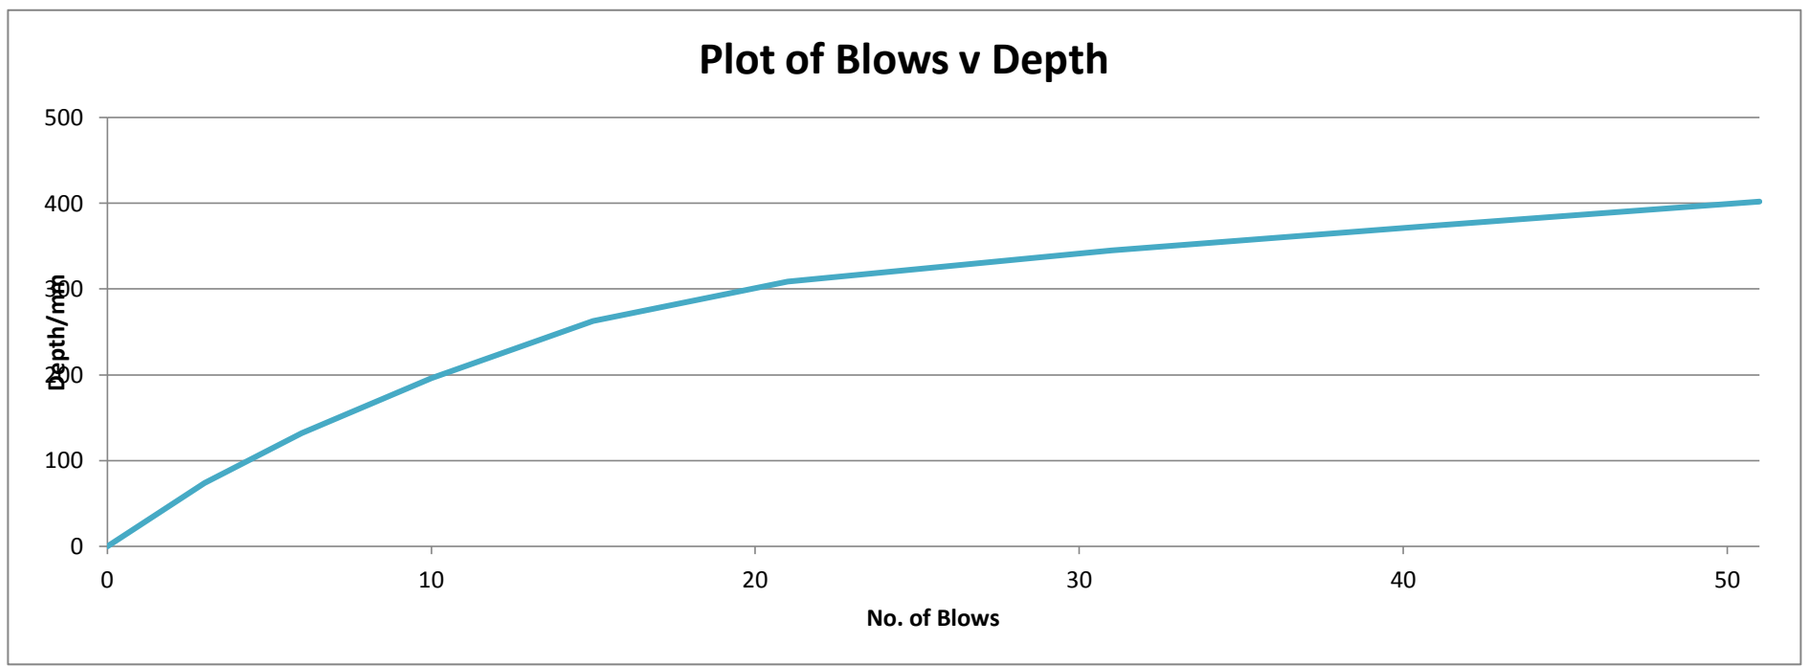

Dynamic Cone Penetration Test (DCPT) for Subgrade Assessment

Project No: 72302
Site: Royston
Test Location: DCP4
Date: 24/06/2014

Title	DCP4				
start (mm bgl)	**finish (mm bgl)**	**start**	**finish**	**DCP Blows**	**CBR%**
0	100	0	5	5	13
100	200	5	10	5	13
200	300	10	22	12	35
300	400	22	43	21	60
400	500	43	63	20	60

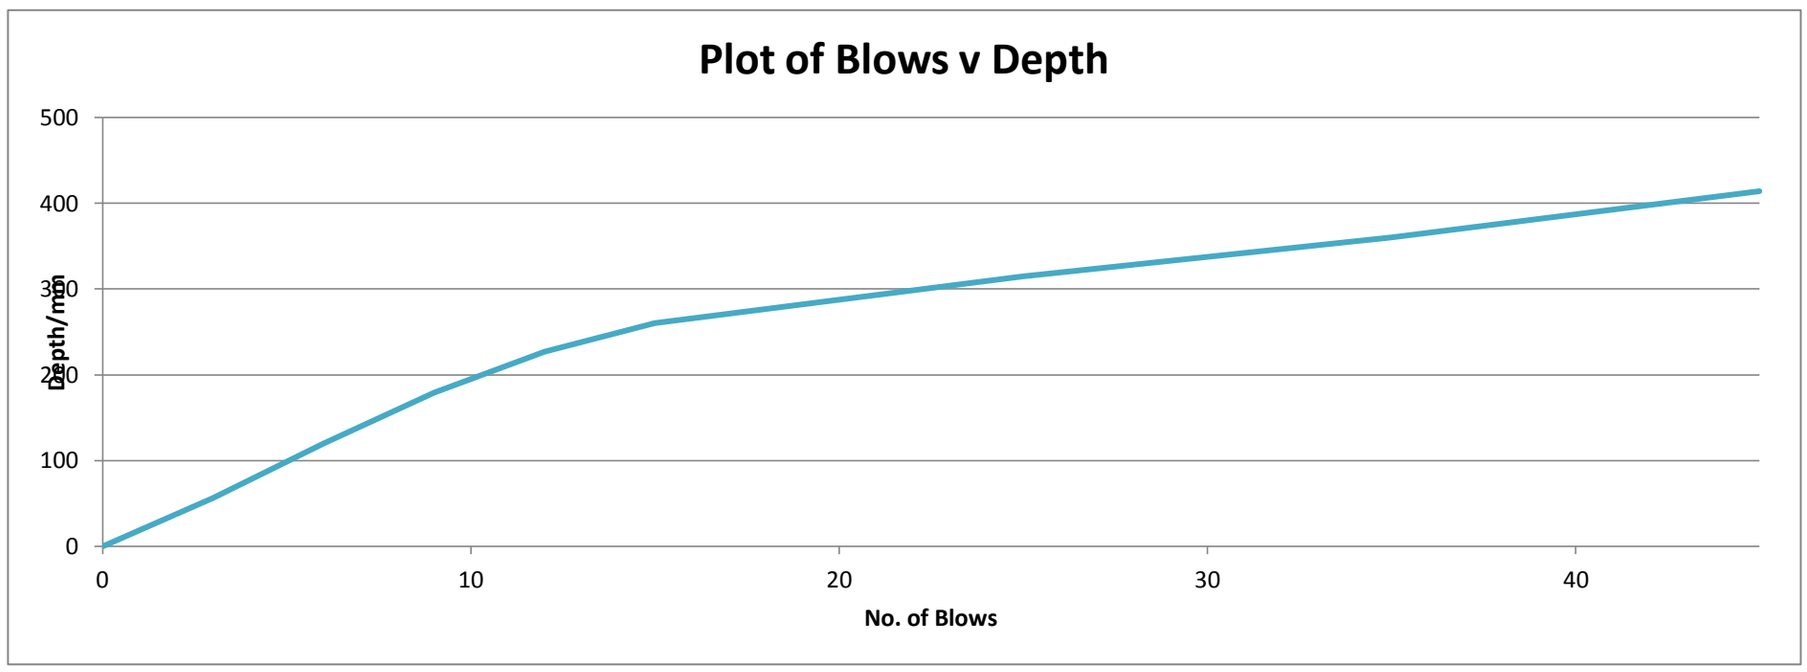

Dynamic Cone Penetration Test (DCPT) for Subgrade Assessment

Project No: 72302
Site: Royston
Test Location: DCP5
Date: 24/06/2014

Title	DCP5				
start (mm bgl)	finish (mm bgl)	start	finish	DCP Blows	CBR%
0	100	0	5	5	13
100	200	5	9	4	10
200	300	9	15	6	16
300	400	15	20	5	13
400	500	20	27	7	18
500	600	27	36	9	23

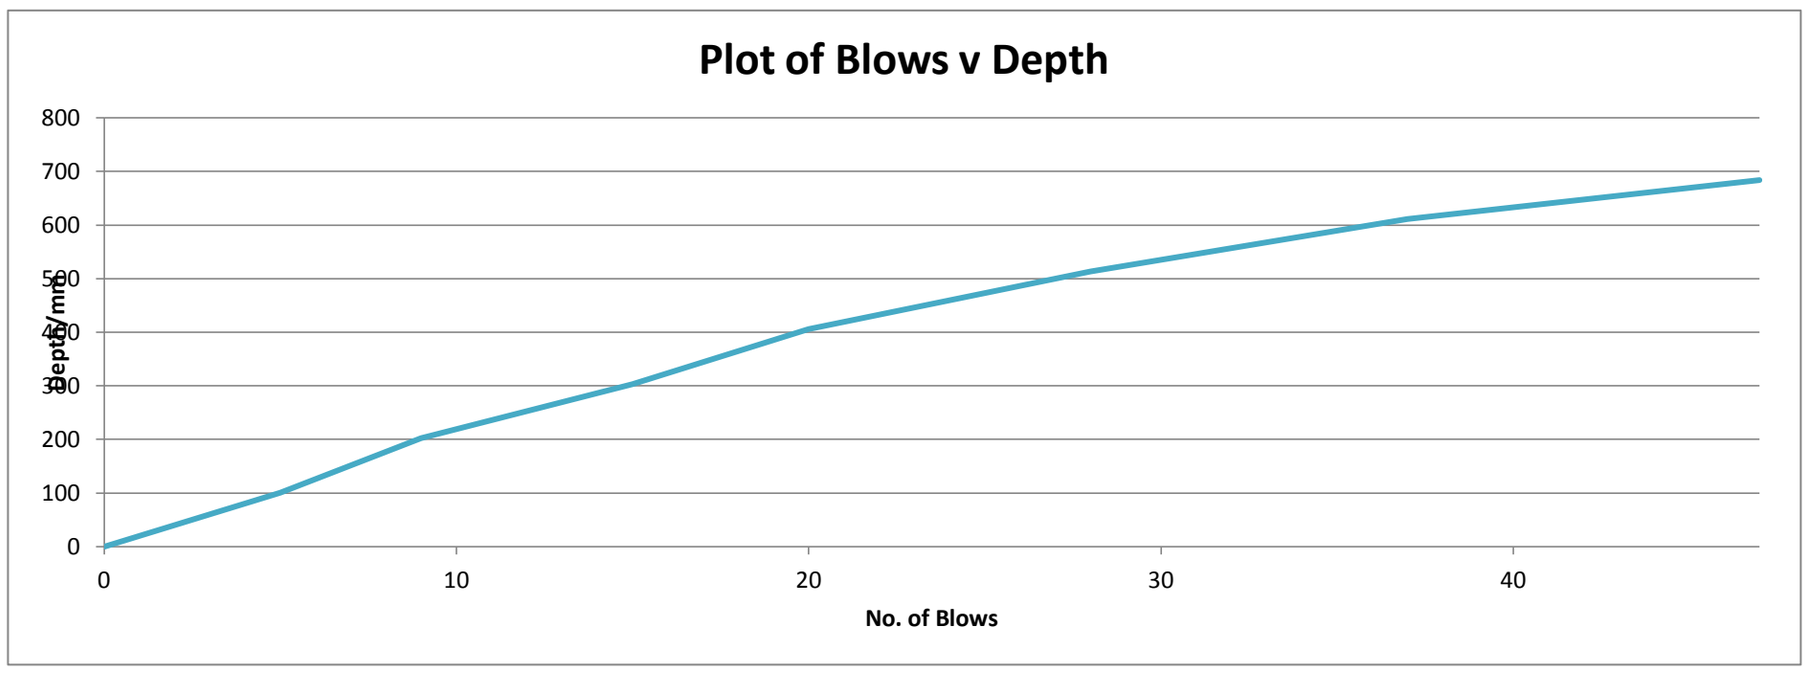

Dynamic Cone Penetration Test (DCPT) for Subgrade Assessment

Project No: 72302
Site: Royston
Test Location: DCP6
Date: 24/06/2014

Title	DCP6				
start (mm bgl)	**finish (mm bgl)**	**start**	**finish**	**DCP Blows**	**CBR%**
0	100	0	2	2	3.5
100	200	2	8	6	16
200	300	8	33	25	60
300	400	33	86	53	60

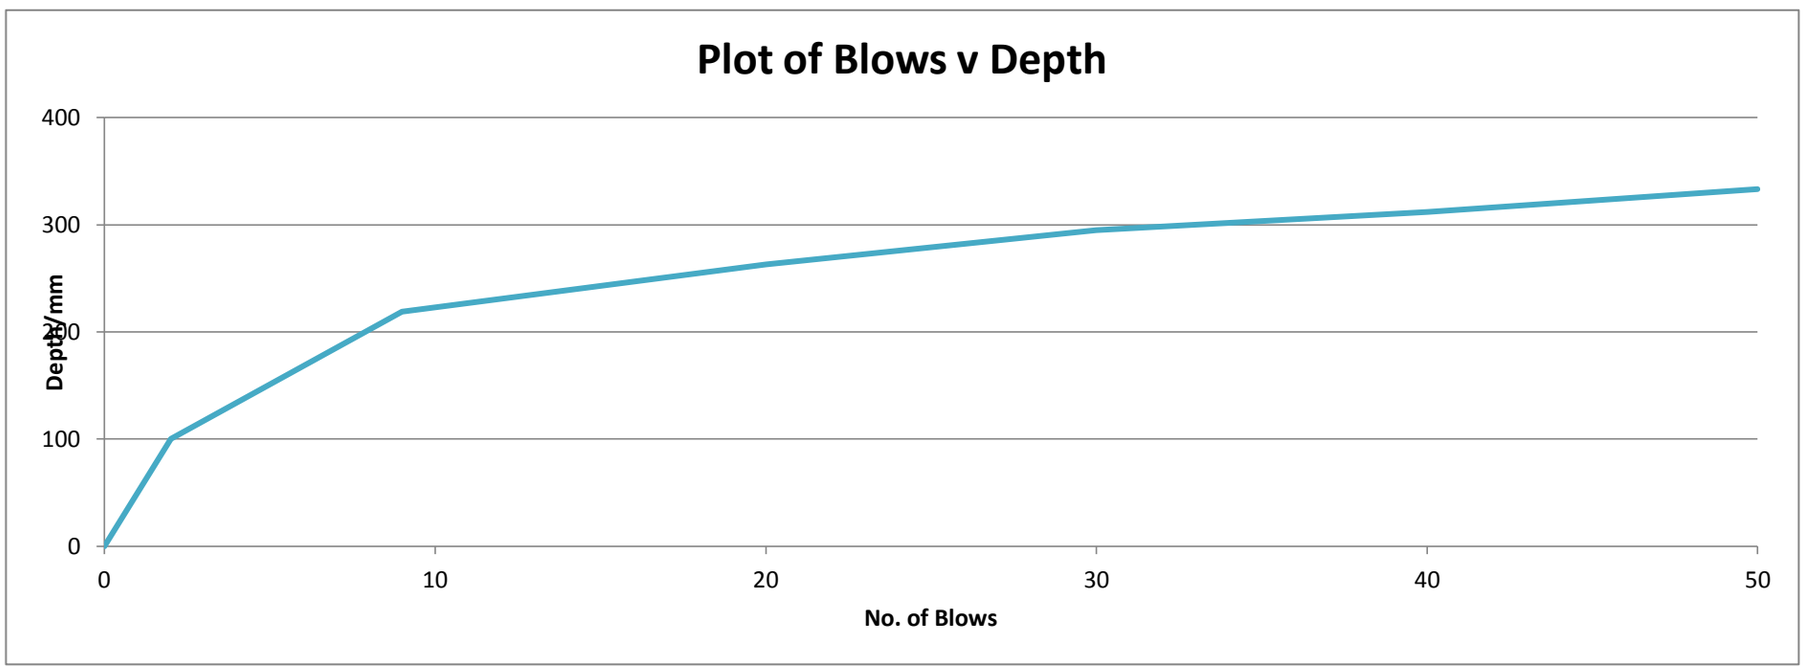

Dynamic Cone Penetration Test (DCPT) for Subgrade Assessment

Project No: 72302
Site: Royston
Test Location: DCP7
Date: 24/06/2014

Title	DCP7				
start (mm bgl)	**finish (mm bgl)**	**start**	**finish**	**DCP Blows**	**CBR%**
0	100	0	4	4	10
100	200	4	12	8	22
200	300	12	29	17	48
300	400	29	46	17	48

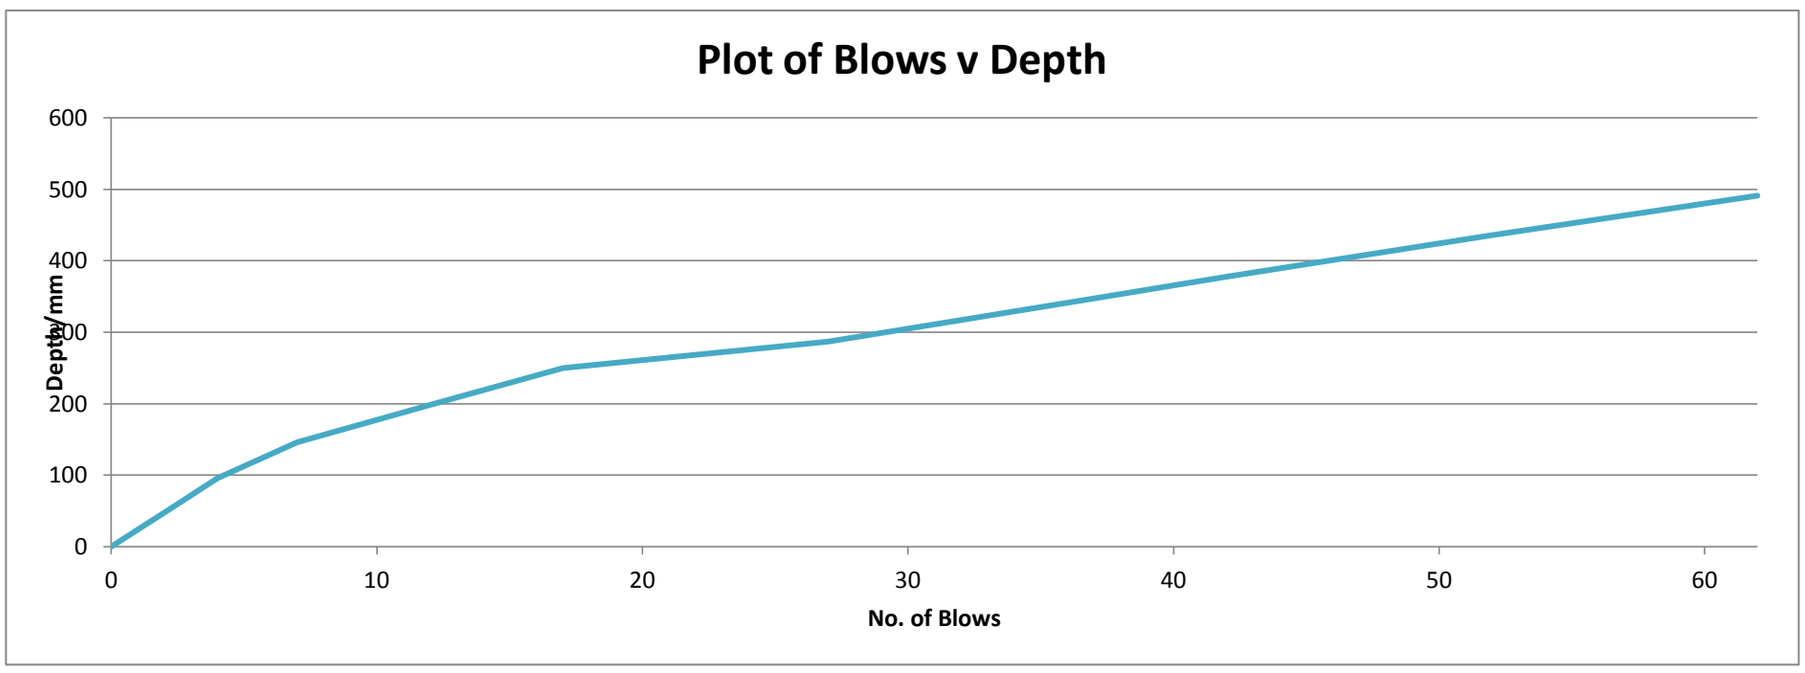

Dynamic Cone Penetration Test (DCPT) for Subgrade Assessment

Project No: 72302
Site: Royston
Test Location: DCP8
Date: 24/06/2014

Title	DCP8				
start (mm bgl)	finish (mm bgl)	start	finish	DCP Blows	CBR%
0	100	0	6	6	16
100	200	6	11	5	13
200	300	11	16	5	13
300	400	16	26	10	25

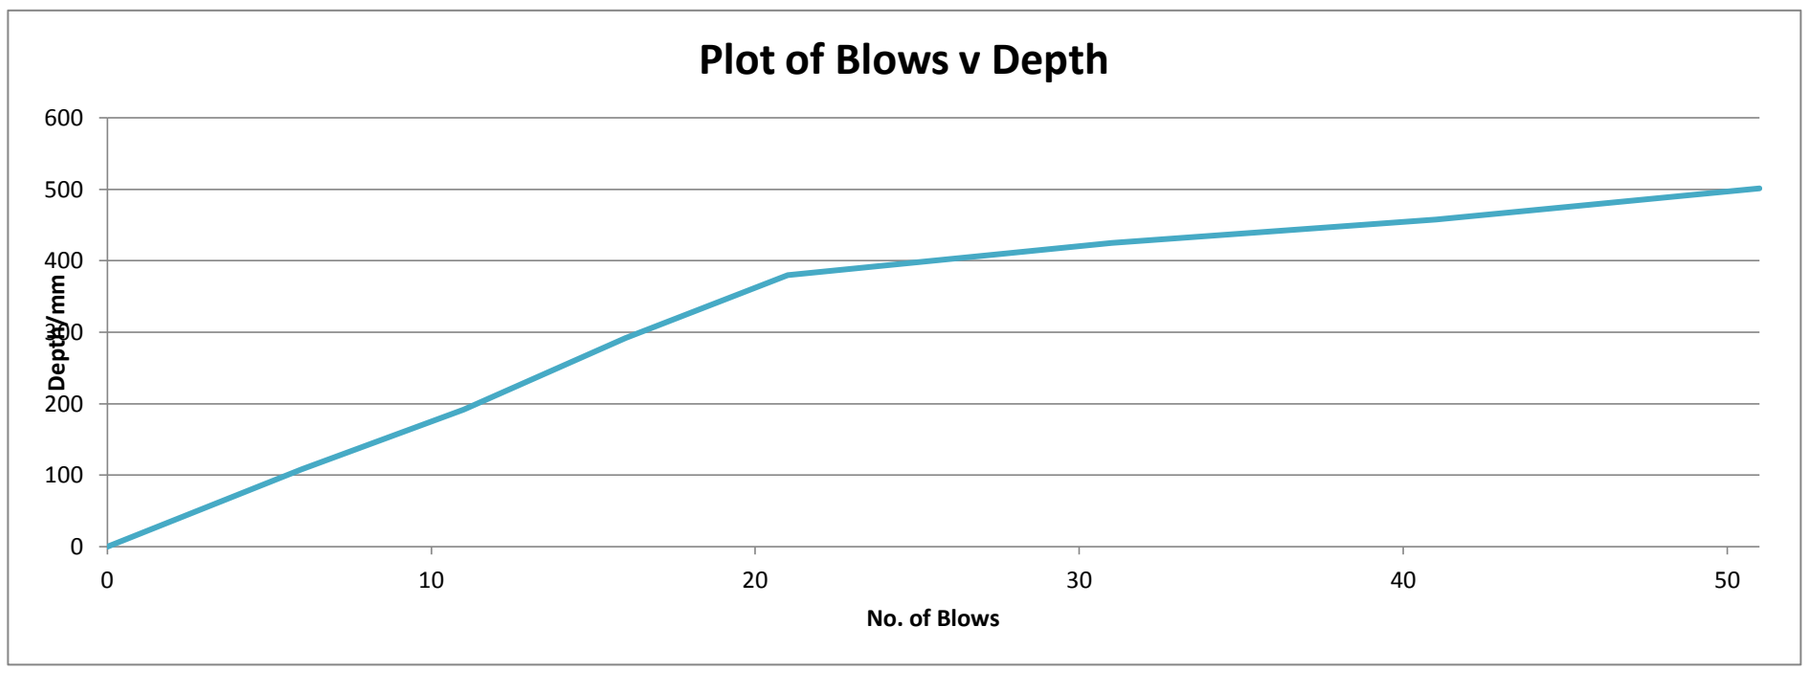

Dynamic Cone Penetration Test (DCPT) for Subgrade Assessment

Project No: 72302
Site: Royston
Test Location: DCP9
Date: 24/06/2014

Title	DCP9				
start (mm bgl)	finish (mm bgl)	start	finish	DCP Blows	CBR%
0	100	0	4	4	10
100	200	4	8	4	10
200	300	8	11	3	6
300	400	11	15	4	10
400	500	15	21	6	16
500	600	21	32	11	30

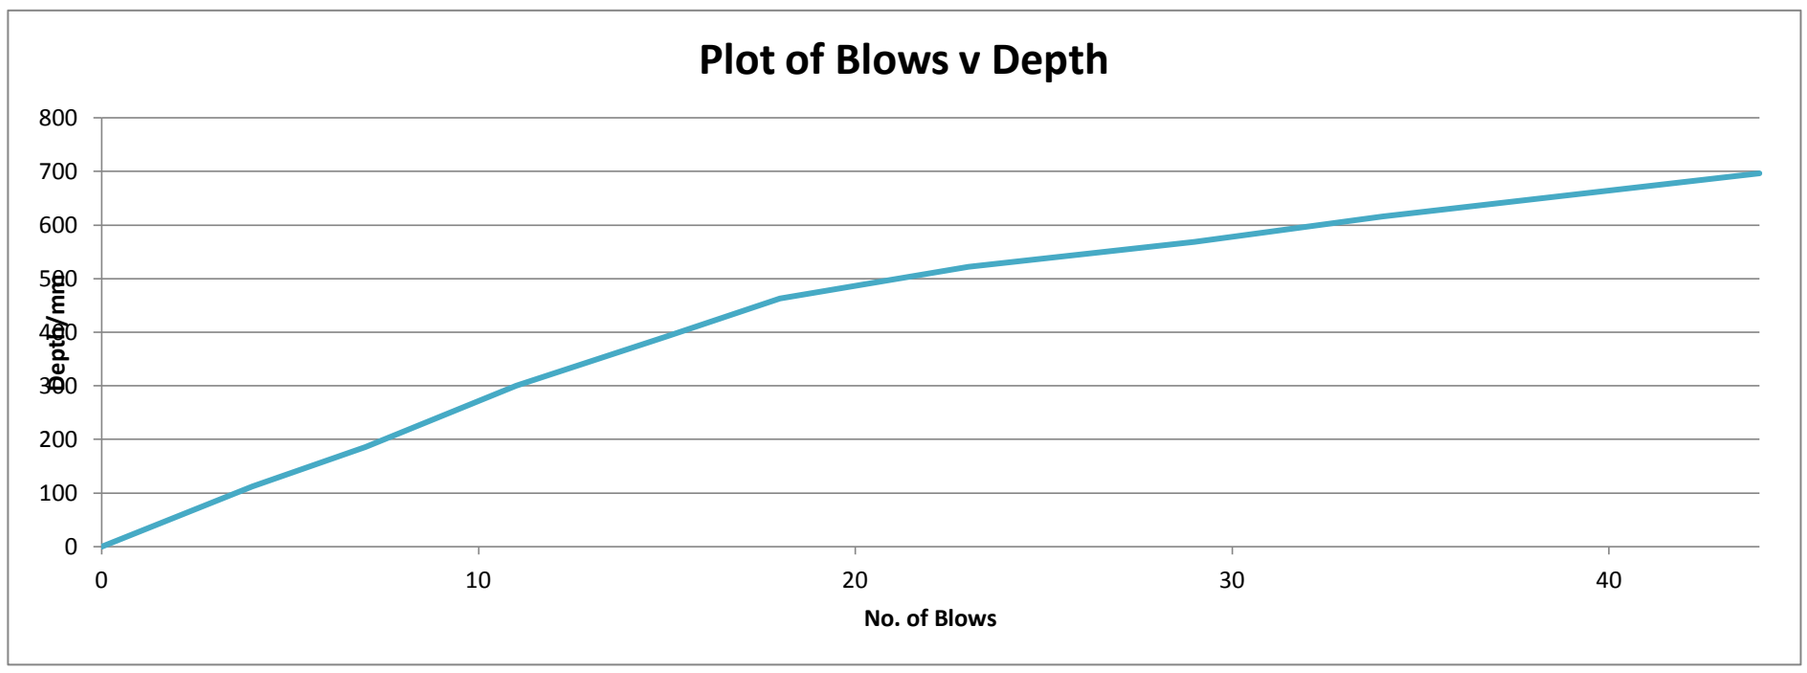

Dynamic Cone Penetration Test (DCPT) for Subgrade Assessment

Project No: 72302
Site: Royston
Test Location: DCP10
Date: 24/06/2014

Title	DCP10				
start (mm bgl)	finish (mm bgl)	start	finish	DCP Blows	CBR%
0	100	0	4	4	10
100	200	4	10	6	16
200	300	10	15	5	13
300	400	15	21	6	16
400	500	21	39	18	55

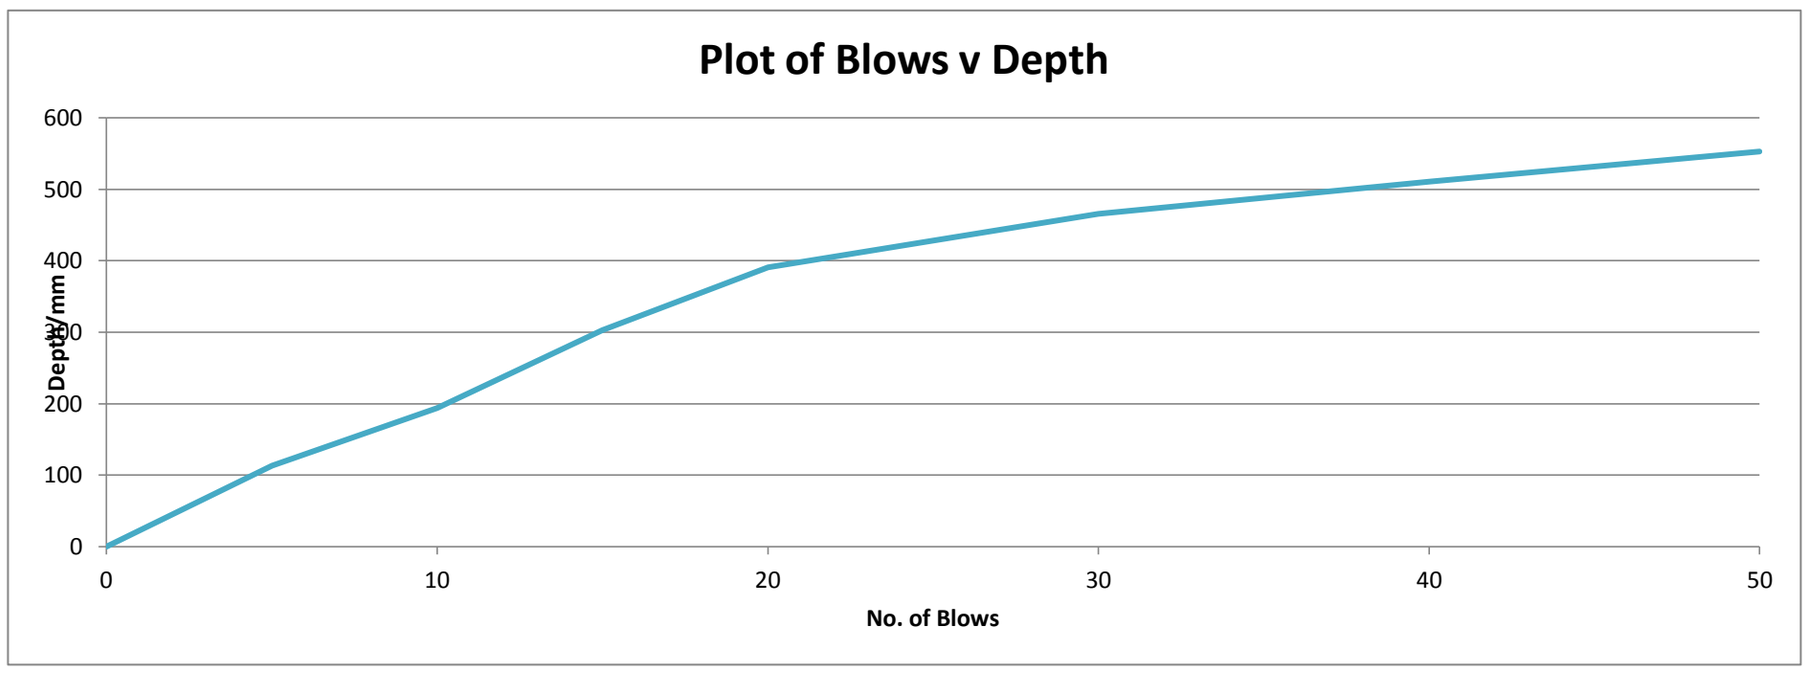

Dynamic Cone Penetration Test (DCPT) for Subgrade Assessment

Project No: 72302
Site: Royston
Test Location: DCP11
Date: 24/06/2014

Title	DCP11				
start (mm bgl)	**finish (mm bgl)**	**start**	**finish**	**DCP Blows**	**CBR%**
0	100	0	7	7	18
100	200	7	13	6	16
200	300	13	17	4	10
300	400	17	21	4	10
400	500	21	25	4	10
500	600	25	31	6	16
600	700	31	41	10	25
700	800	41	52	11	30

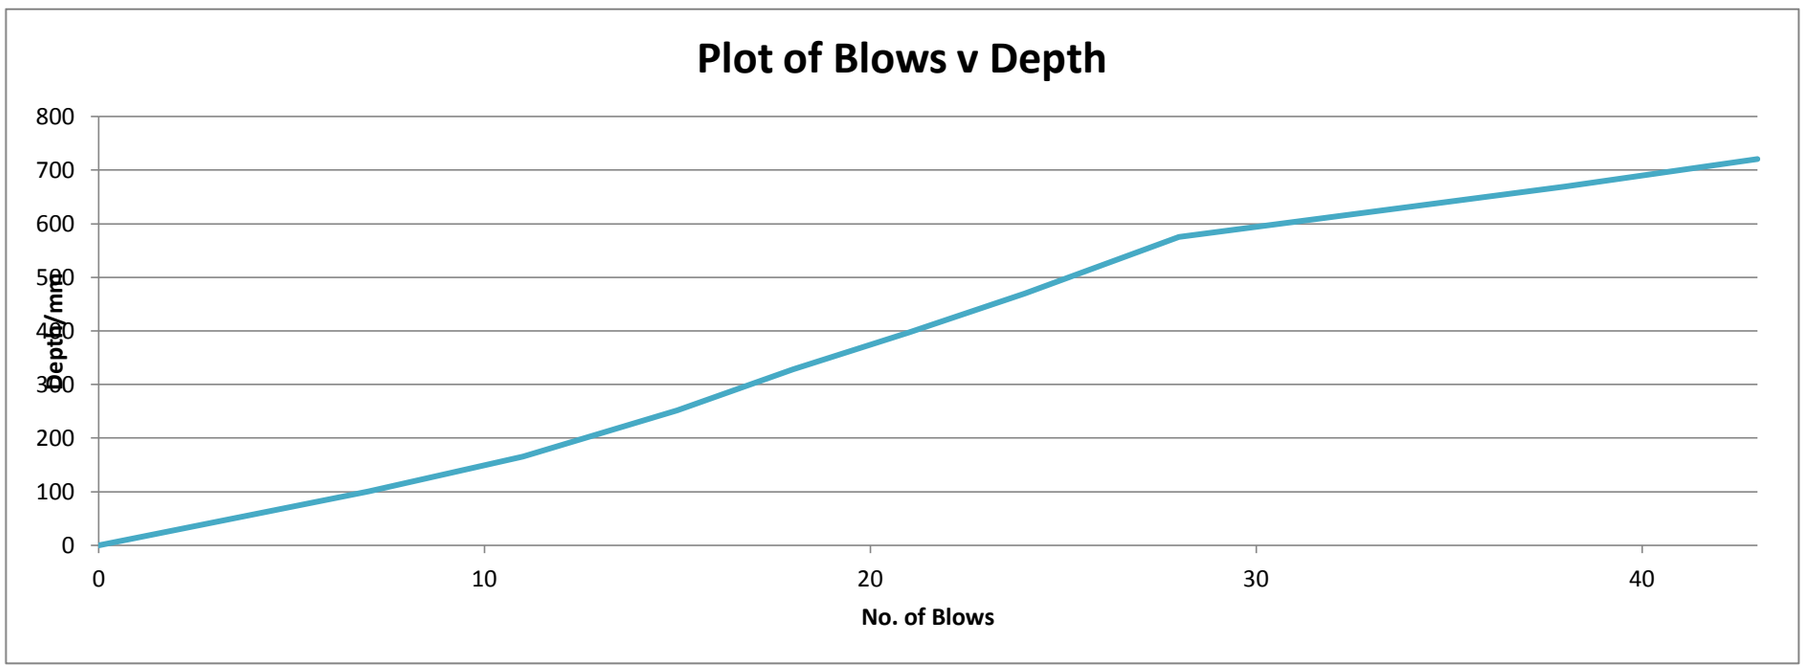

Dynamic Cone Penetration Test (DCPT) for Subgrade Assessment

Project No: 72302
Site: Royston
Test Location: DCP12
Date: 24/06/2014

Title	DCP12				
start (mm bgl)	**finish (mm bgl)**	**start**	**finish**	**DCP Blows**	**CBR%**
0	100	0	1	1	1
100	200	1	3	2	3.5
200	300	3	8	5	13
300	400	8	21	13	40

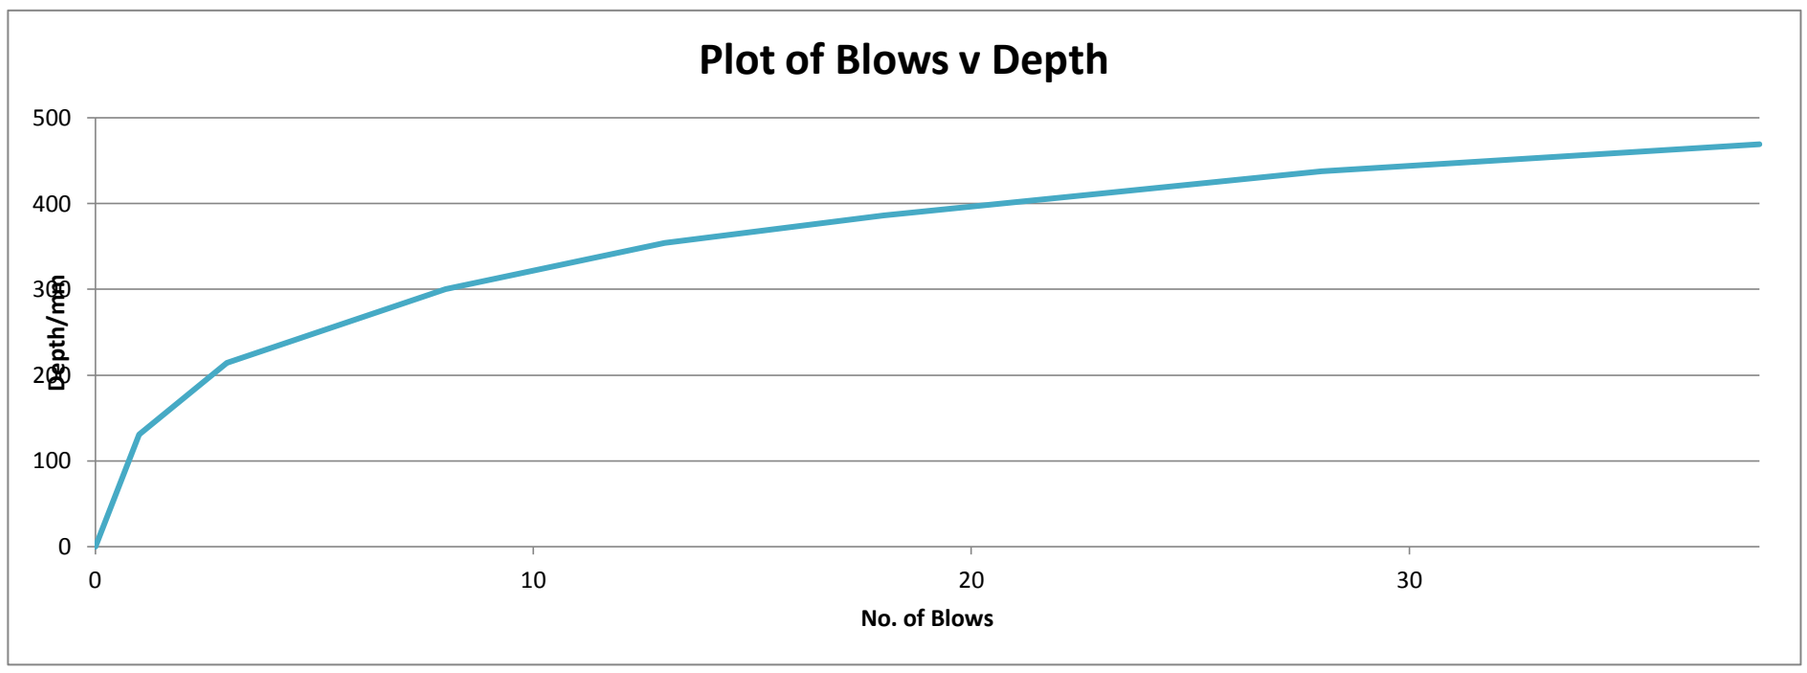

Dynamic Cone Penetration Test (DCPT) for Subgrade Assessment

Project No: 72302
Site: Royston
Test Location: DCP13
Date: 24/06/2014

Title	DCP13				
start (mm bgl)	finish (mm bgl)	start	finish	DCP Blows	CBR%
0	100	0	2	2	3.5
100	200	2	5	3	6
200	300	5	14	9	23
300	400	14	25	11	30
400	500	25	39	14	40
500	600	39	64	25	60

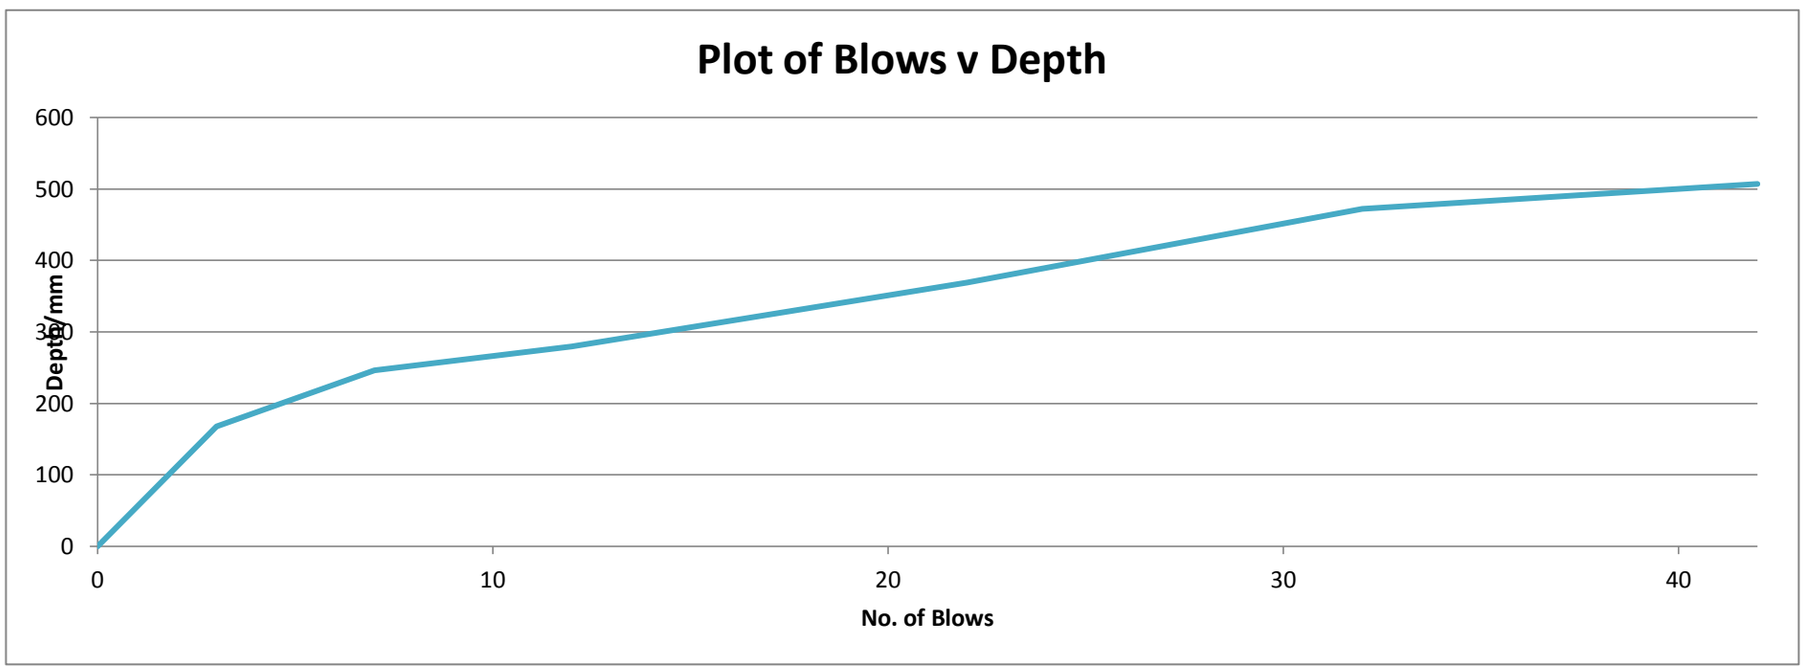

Dynamic Cone Penetration Test (DCPT) for Subgrade Assessment

Project No: 72302
Site: Royston
Test Location: DCP14
Date: 24/06/2014

Title	DCP14				
start (mm bgl)	**finish (mm bgl)**	**start**	**finish**	**DCP Blows**	**CBR%**
0	100	0	1	1	1
100	200	1	7	6	16

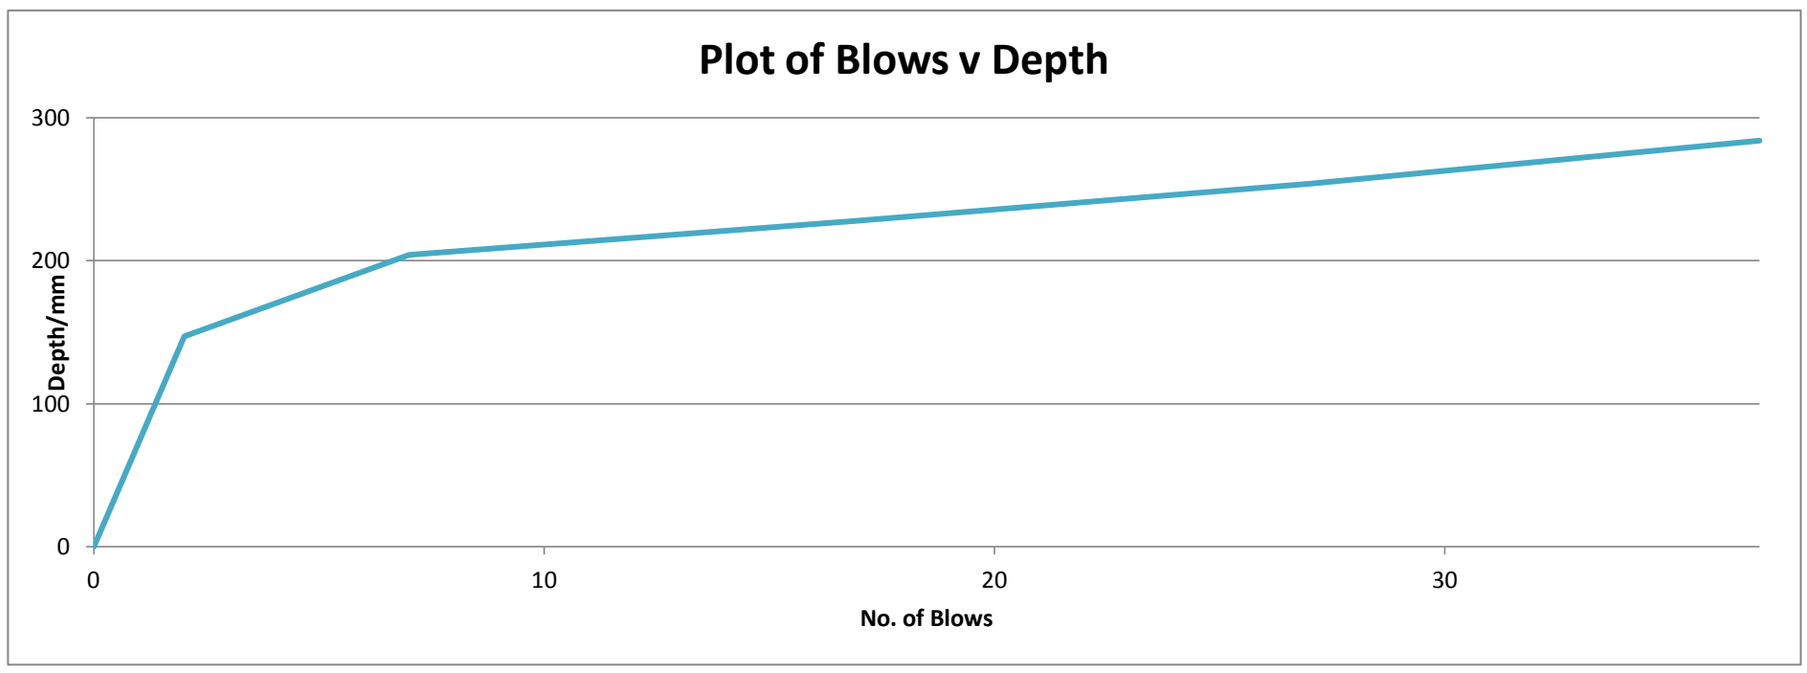

Dynamic Cone Penetration Test (DCPT) for Subgrade Assessment

Project No: 72302
Site: Royston
Test Location: DCP15
Date: 24/06/2014

Title	DCP15				
start (mm bgl)	**finish (mm bgl)**	**start**	**finish**	**DCP Blows**	**CBR%**
0	100	0	4	4	10
100	200	4	10	6	16
200	300	10	34	24	60
300	400	34	64	30	60

