Line	Name	Duration	Start	Finish
1	Reduced Dig	1w	06 Oct 25	10 Oct 25
2	Service Ducts	1d	10 Oct 25	10 Oct 25
3	Soakaway	2d	13 Oct 25	14 Oct 25
4	Hardstanding	3d	15 Oct 25	17 Oct 25
5	Piling Matt	1d	17 Oct 25	17 Oct 25
6	Set Out Piles	1d	27 Oct 25	27 Oct 25
7	Piling Works	2w	27 Oct 25	07 Nov 25
8	Drainage Connections	1w	10 Nov 25	14 Nov 25
9	Slab Works	1w	17 Nov 25	21 Nov 25
10	Site Setup/ Cabins	3d	22 Oct 25	24 Oct 25
11	Brickwork to Joist	3w 2d	24 Nov 25	16 Dec 25
12	Scaffold		08 Dec 25	08 Dec 25
13	Steels	3d	17 Dec 25	19 Dec 25
14	Joists & Flooring 1st FL	1w 2d	05 Jan 26	13 Jan 26
15	Brickwork to Plate	2w	14 Jan 26	27 Jan 26
16	Joists & Flooring 2nd FL	1w	28 Jan 26	03 Feb 26
17	Roof Timbers	2w 4d	28 Jan 26	16 Feb 26
18	Form Dormer	1w	04 Feb 26	10 Feb 26
19	Roof Tile	3w	17 Feb 26	09 Mar 26
20	Fit Staircase	1w	10 Mar 26	16 Mar 26
21	Gutters/ Downpipes	1w 1d	10 Mar 26	17 Mar 26
22	Fit Windows	2w	10 Mar 26	23 Mar 26
23	1st Fix Carpentry	3w	17 Mar 26	08 Apr 26
24	Drop Scaffold		24 Mar 26	24 Mar 26
25	Fit Bifolds	1w	24 Mar 26	01 Apr 26
26	Fit Front Door	1w	02 Apr 26	08 Apr 26
27	UF Heating / Insulation GF	1w	02 Apr 26	08 Apr 26
28	1st Fix Plumbing	1w	09 Apr 26	15 Apr 26
29	Floor Screed	1w	09 Apr 26	15 Apr 26
30	1st Fix Electrical/ MVHR	2w	16 Apr 26	29 Apr 26
31	Insulation/ Tacking/ Plastering	2w 4d	30 Apr 26	20 May 26
32	Mist Coat	1w	21 May 26	28 May 26
33	Tile Kitchen	1w	29 May 26	04 Jun 26
34	Fit Kitchen	2w	05 Jun 26	18 Jun 26
35	2nd Fix Carpentry	2w	12 Jun 26	25 Jun 26
36	Template/ Fit Quartz Kitchen		19 Jun 26	19 Jun 26
37	Bathroom Tiling	1w	19 Jun 26	25 Jun 26
38	Wardrobes	1w	26 Jun 26	02 Jul 26
39	2nd Fix Plumbing	1w	26 Jun 26	02 Jul 26
40	2nd Fix Electrical / Alarm	1w	03 Jul 26	09 Jul 26
41	Decoration	2w	10 Jul 26	23 Jul 26
42	Finals	1w	24 Jul 26	30 Jul 26
43	Carpets	1w	31 Jul 26	06 Aug 26
44	Clean	1w	07 Aug 26	13 Aug 26
45	Snagging & Handover	1w	14 Aug 26	20 Aug 26
46	SWTP Intall	1w	03 Mar 26	09 Mar 26
47	Water connection	1w	03 Mar 26	09 Mar 26
48	Electrical connection	1w	10 Mar 26	16 Mar 26
49	Foul connection	1w	17 Mar 26	23 Mar 26
50	BT Connection	1w	24 Mar 26	01 Apr 26
51	Call off/ Connect Meters		24 Jul 26	24 Jul 26
52	Topsoil Level/ Spread Rear	1w	06 Apr 26	10 Apr 26
53	Side Paving/ Finishes	3w	09 Apr 26	29 Apr 26
54	Rear Patios	2w 4d	15 Apr 26	05 May 26
55	Install car charging	1w	30 Apr 26	07 May 26
56	Block paving - Driveway/ Parking	3w	08 May 26	29 May 26
57	Fencing	2w	05 Jun 26	18 Jun 26
58	Topsoil Level/ Spread Front	1w	03 Jul 26	09 Jul 26
59	Landscaping/ Planting	2w	10 Jul 26	23 Jul 26
60	Turf	1w	24 Jul 26	30 Jul 26

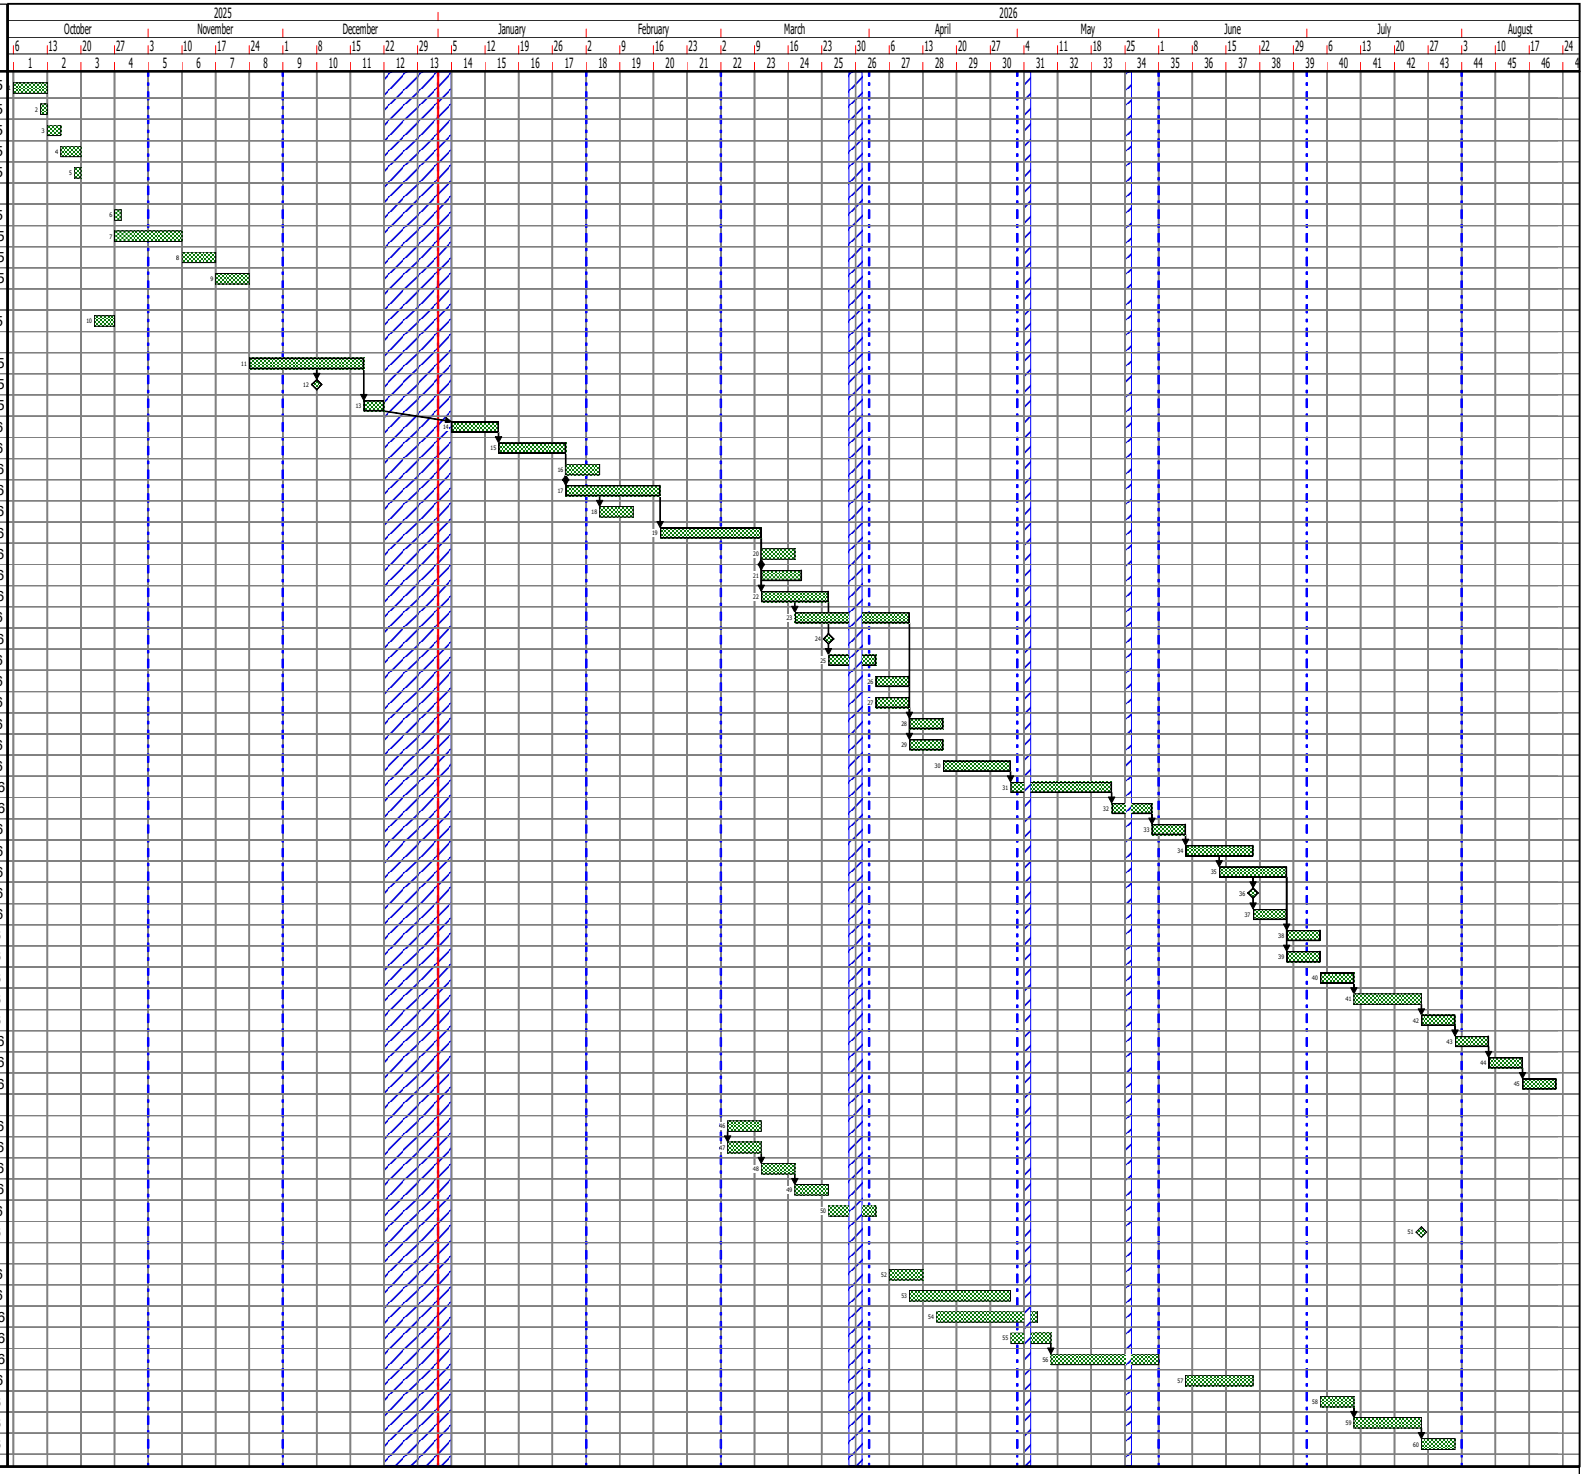

Trades Contractor

Default

Milestone Appearances

Diamond
